


DEPARTMENT OF CIVIL ENGINEERING



MS PROJECT LAB MANUAL

**(FOR 6TH SEMESTER CIVIL ENGINEERING STUDENTS UNDER
SCTE&VT, ODISHA, BHUBANESWAR)**

JHARSUGUDA ENGINEERING SCHOOL, JHARSUGUDA



DEPARTMENT OF CIVIL ENGINEERING

VISION

To produce competent and capable Civil Engineering professionals by imparting excellent quality and skill based technical education, moral values and ethics for serving the society.

Mission

- ❖ To provide knowledge of various Civil Engineering aspects and skill based practices with modern technique and methods in collaboration with industry by providing state-of-the-art lab facilities pertaining to the curriculum on par with the best to make future Civil Engineers.
- ❖ To inculcate ethical values & professionalism among the students.
- ❖ To promote the spirit of enquiry, innovation, life skills and to encourage entrepreneurship.

Program Educational Objectives

- ❖ To apply technical knowledge and management principles in analyzing and planning problems in the field of Civil Engineering, while ensuring maximization of economic benefits to society and minimization of damage to ecology and environment.
- ❖ To enhance entrepreneurial, communications and other soft skills in such a way that they can be successful as entrepreneurs, pursue higher studies so that they can contribute to the research and development of Civil Engineering and other allied fields.
- ❖ To make students committed to highest level of professional ethics such that they should function effectively in the multicultural and multidisciplinary groups for the sustainable development and growth of Civil Engineering projects and profession.

Objectives


- Projects management Basics
- Getting started with MS Project
- Creating a project (Tasks, Resources, ...)
- Views and Reports

A Project is

A temporary endeavor undertaken to create a unique product, service, or result.

Project Life Cycle (Phases)

- Initiation
- Planning
- Execution
- Closure

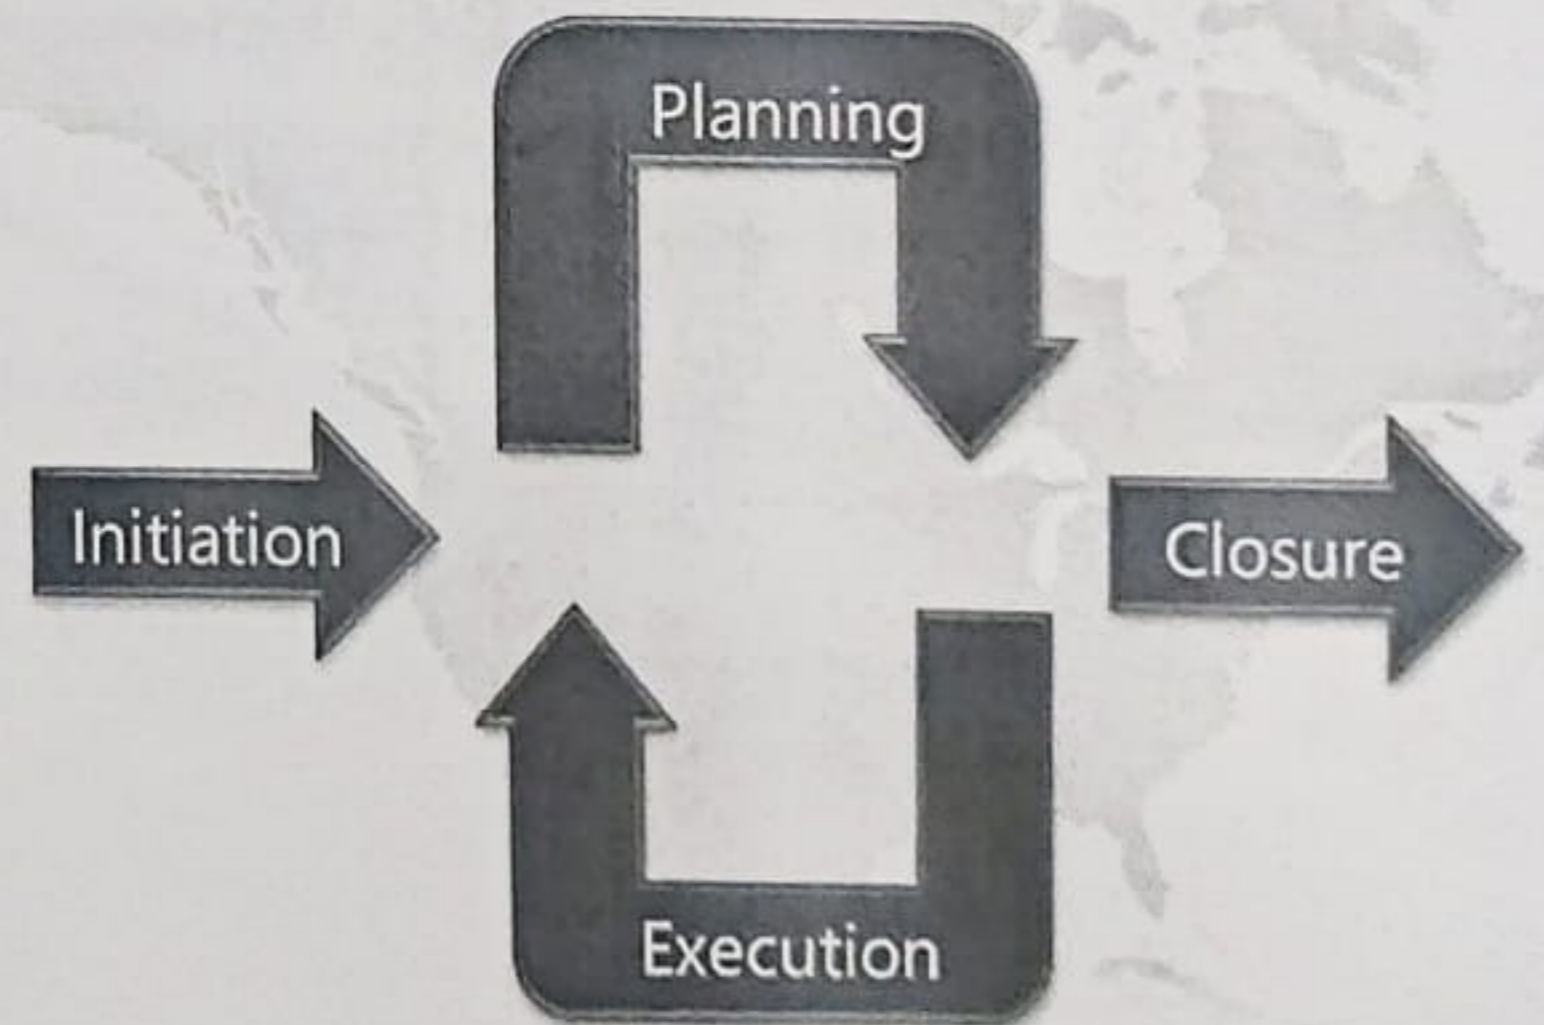


Projects Management is

The application of knowledge, skills, tools, and techniques to project activities, in order to meet or exceed stakeholder needs and expectations from a defined project - balancing the following:

- Scope, time, cost, and quality
- Stakeholders' expectations
- Requirements (needs) vs. unidentified requirements (expectations)

PM Process Groups

- Initiating
- Planning
- Executing
- Monitoring and Controlling
- Closing

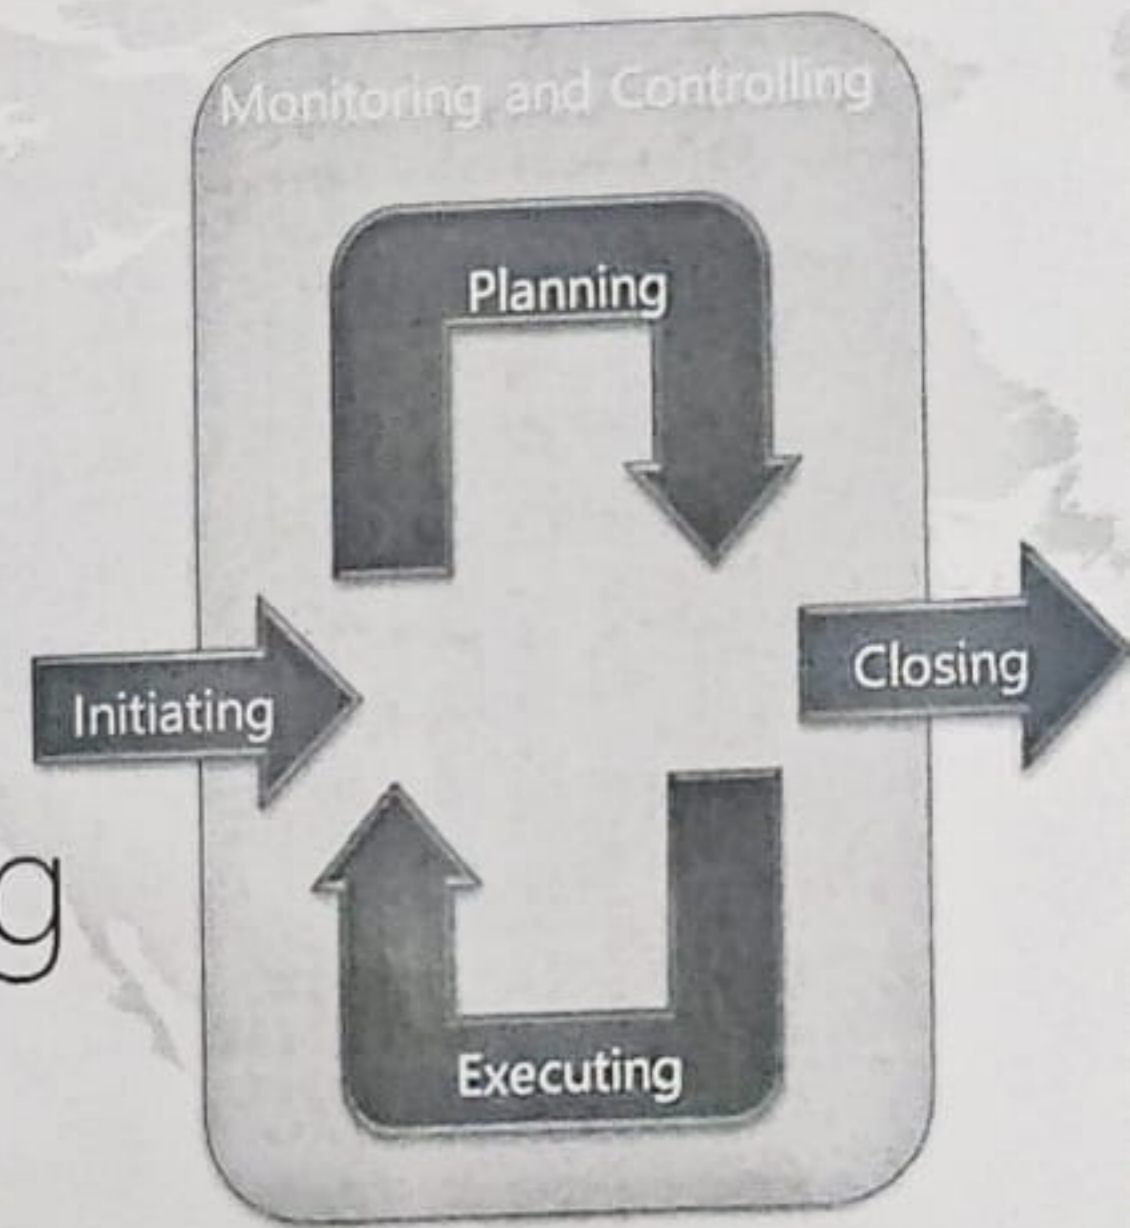

Project Life Cycle with PM


Initiating

Planning

Executing

Closing


Monitoring

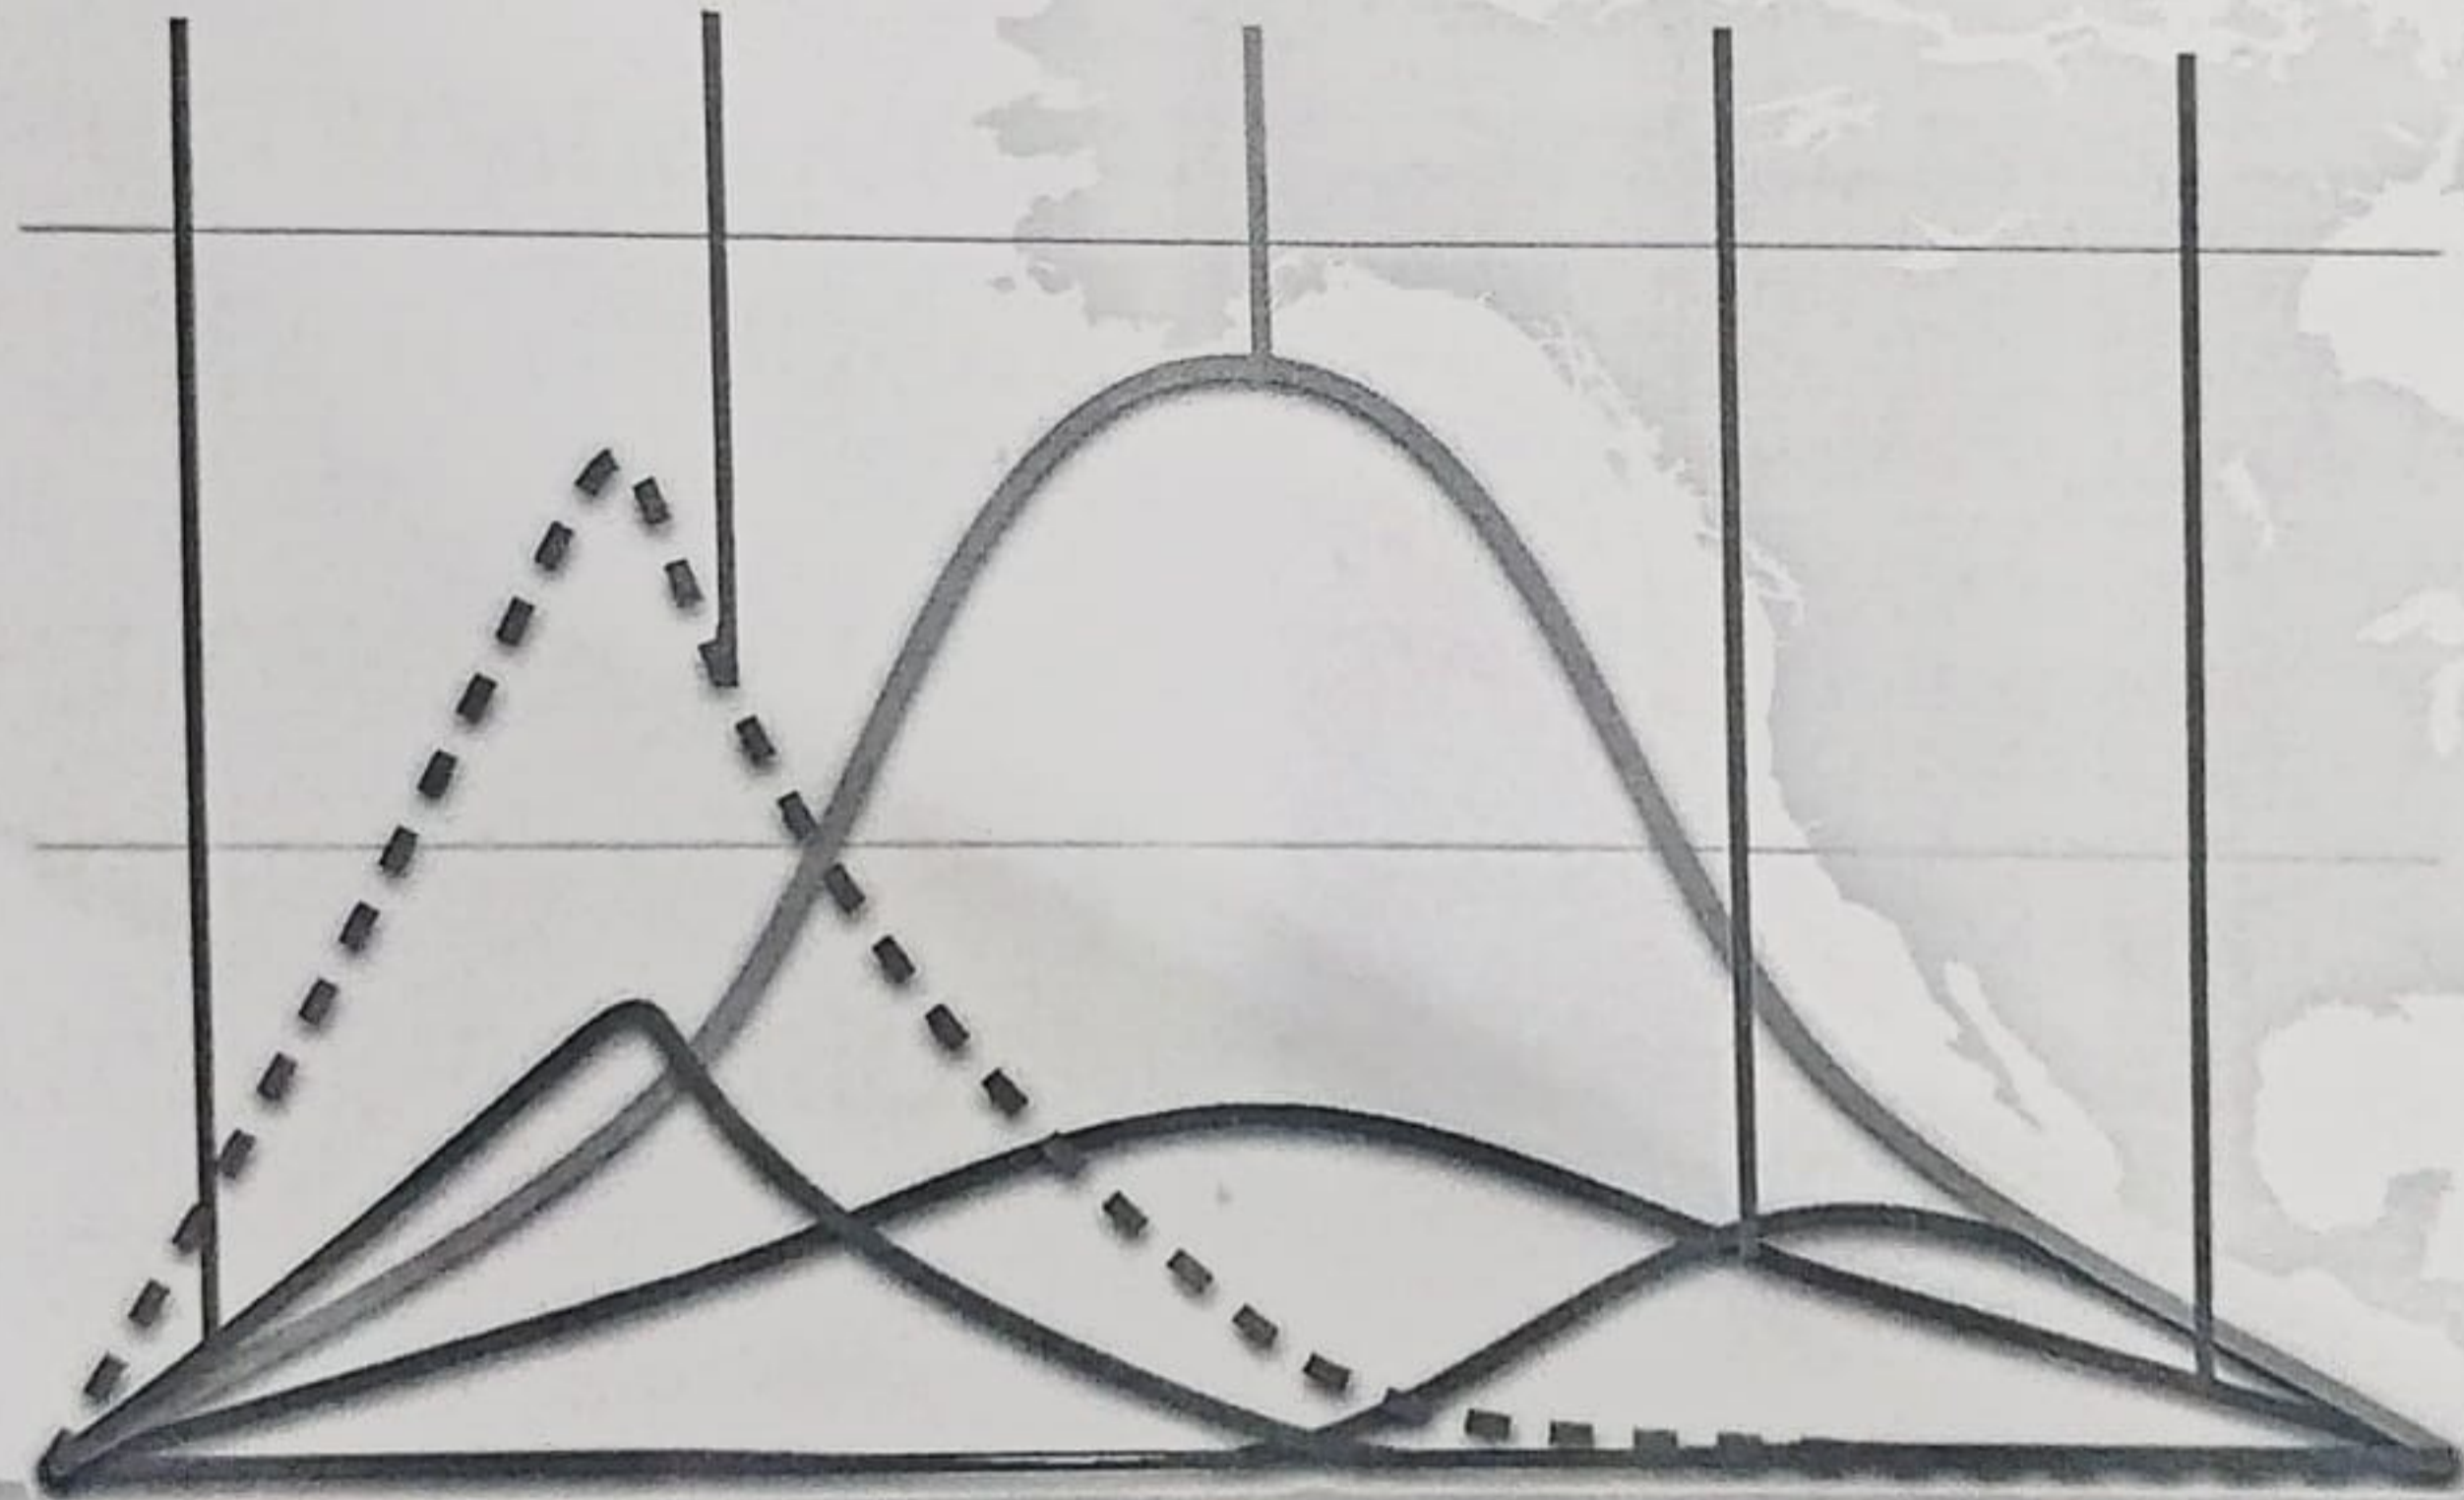

Project Manager

A project manager is a professional in the field of project management.

Project managers can have the responsibility of the planning, execution, and closing of any project.



MS Project

Microsoft Project is a project management software program, which is designed to assist a project manager in developing a plan, assigning resources to tasks, tracking progress, managing the budget, and analysing workloads.

Note

Microsoft project expert isn't a replacement for the project manager.

Microsoft Project doesn't ensure a successful project if a person doesn't understand project management. However, Microsoft Project can assist a project manager in becoming more effective.

Setting working Days

The screenshot shows the Microsoft Project Professional interface. The 'Project' ribbon is active, with the 'Change Working Time' button highlighted by a hand cursor. The background shows a Gantt chart area with a task named 'Task 1' starting on 'Mon 16-02-08'. The status bar at the bottom indicates 'Ready' and 'New Tasks: Manually Scheduled'.

Change Working Time

For calendar: Standard (Project Calendar) Create New Calendar...

Calendar: Standard (Project Calendar)

Legend:

- Working
- Nonworking
- 31 Edited working hours
- 31 Exception day
- 31 Nondefault work week

Click on a day to see its working times:

2016 February

| S | M | T | W | Th | F | S |
|----|----|----|----|----|----|----|
| | 1 | 2 | 3 | 4 | 5 | 6 |
| 7 | 8 | 9 | 10 | 11 | 12 | 13 |
| 14 | 15 | 16 | 17 | 18 | 19 | 20 |
| 21 | 22 | 23 | 24 | 25 | 26 | 27 |
| 28 | 29 | | | | | |
| | | | | | | |

Working times for 2016 February 08:

- 8:00 AM to 12:00 PM
- 1:00 PM to 5:00 PM

Based on: Default work week on calendar Standard.

Exceptions

| Name | Start | Finish |
|------|-------|--------|
| | | |
| | | |
| | | |
| | | |
| | | |
| | | |
| | | |
| | | |
| | | |
| | | |
| | | |

Buttons: Help, Options..., OK, Cancel

Schedule a Project from a Start or Finish Dates

The screenshot displays the Microsoft Project Professional (Trial) interface. The main window is titled "Project1 - Project Professional (Trial)" and shows the "Project" tab selected in the ribbon. The ribbon includes options like "Project Information", "Custom Fields", "Links Between Projects", "WBS", "Change Working Time", "Calculate Project Baseline", and "Move". The "Project Information" dialog box is open, showing the following settings:

- Start date: Mon 16-01-01
- Current date: Mon 16-02-08
- Finish date: Mon 16-02-08
- Status date: NA
- Schedule from: Project Start Date
- Calendar: Standard
- All tasks begin as soon as possible.
- Priority: 500
- Enterprise Custom Fields: Department (empty)


The dialog box also features a table for "Enterprise Custom Fields" with columns for "Custom Field Name" and "Value". At the bottom of the dialog, there are buttons for "Help", "Statistics...", "OK", and "Cancel".

The MS Project interface

Toolbar

Ribbon

Main Screen components

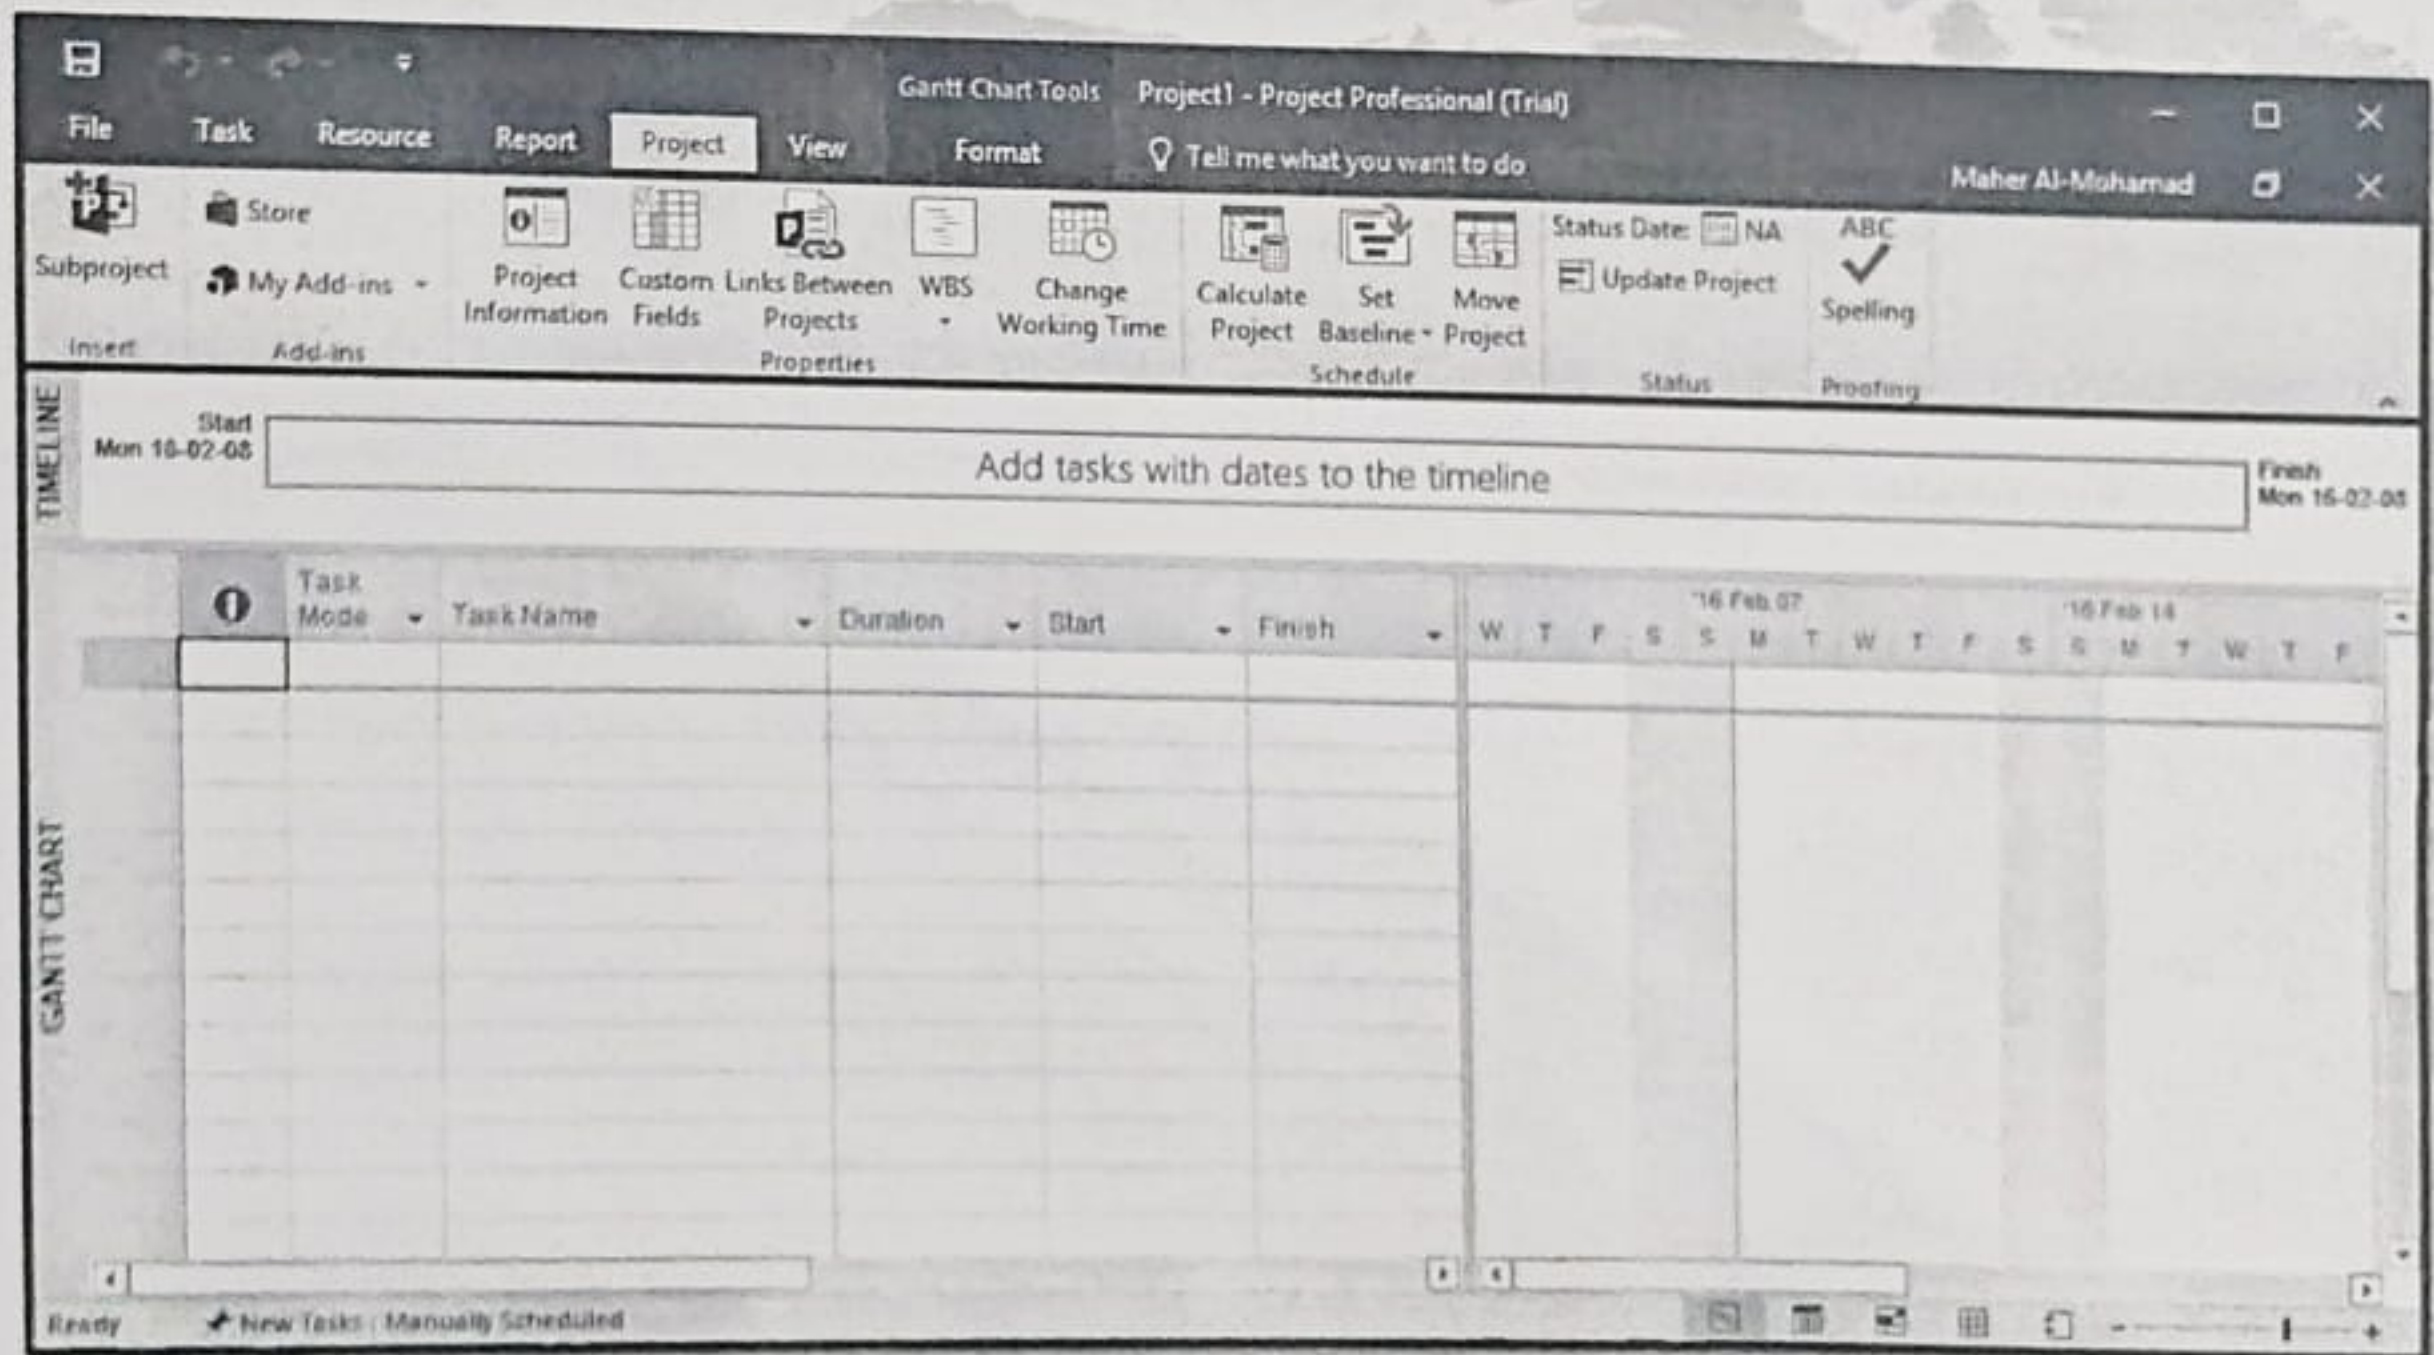

Start a new project


Project


Recent

Pinned

 Diamond.mpp
Desktop


Other


 Software Development Plan.mpt
C:\Users\Maher\AppData\Roaming\Micro...


 Open Other Projects


Search for online templates


Suggested searches: Project Management Project Plan Projects Themes Schedules
Analysis Industry


Maher Al-Mohamad
maher.almohamad@outlook.com
Switch account 


 Blank Project


 New from existing project


 New from Excel workbook


 New from SharePoint Tasks List

 SOFTWARE DEVELOPMENT PLAN
Software Development Plan

 Using Project to Manage your Agile Projects
Agile project management

 CREATE A BUDGET
Create a Budget

 Commercial Construction

 EARNED VALUE \$1,700.00 \$1,700.00
Earned value

Working with Tasks List

Adding the essential data of tasks :

- ✓ Task name
- ✓ Duration (D, W, H, M, Mo)
- ✓ Predecessors


| | Info | Task Mo | Task Name | Duration | Add New Column |
|----|------|---------|--|----------|----------------|
| 1 | ✓ | → | Diamond Implementation Project | 0 days | |
| 2 | | ★ | ▾ Project Preparation | 19 days | |
| 3 | | ★ | 1st Project Kickoff meeting | 1 day | |
| 4 | | ★ | Project Charter | 5 days | |
| 5 | | ★ | Org Structure | 3 days | |
| 6 | | ★ | BRD | 15 days | |
| 7 | | ★ | ▸ Gap Analysis RICEF | 3 days | |
| 14 | | ★ | Sign Off Project Charter | 3 days | |
| 15 | | ★ | ▾ Business Blueprint | 12 days | |
| 16 | | ★ | 2ndProject Kickoff meeting | 1 day | |
| 17 | | ★ | BBP FICO Meetings | 5 days | |
| 18 | | ★ | BBP SD Meetings | 5 days | |
| 19 | | ★ | BBP MM Meetings | 5 days | |
| 20 | | ★ | BBP BI Meetings | 5 days | |
| 21 | | ★ | Business Blueprints Integration Workshop | 5 days | |
| 22 | | ★ | Sign Off Business Blueprints | 1 day | |
| 23 | | ★ | ▾ Realization | 40 days | |
| 24 | | ★ | Project Team Status Meetings | 10 days | |
| 25 | | ★ | System Configuration | 30 days | |
| 26 | | ★ | Training for UT scenarios | 20 days | |
| 27 | | ★ | ▸ RICEF Programs Development | 10 days | |
| 31 | | ★ | Integration Test | 10 days | |
| 32 | | ★ | ▸ Final Preparation | 10 days | |
| 35 | | ★ | ▸ Go Live Support | 2 days? | |

Gantt Chart

Task Spreadsheet

Gantt Diagram

GANTT CHART

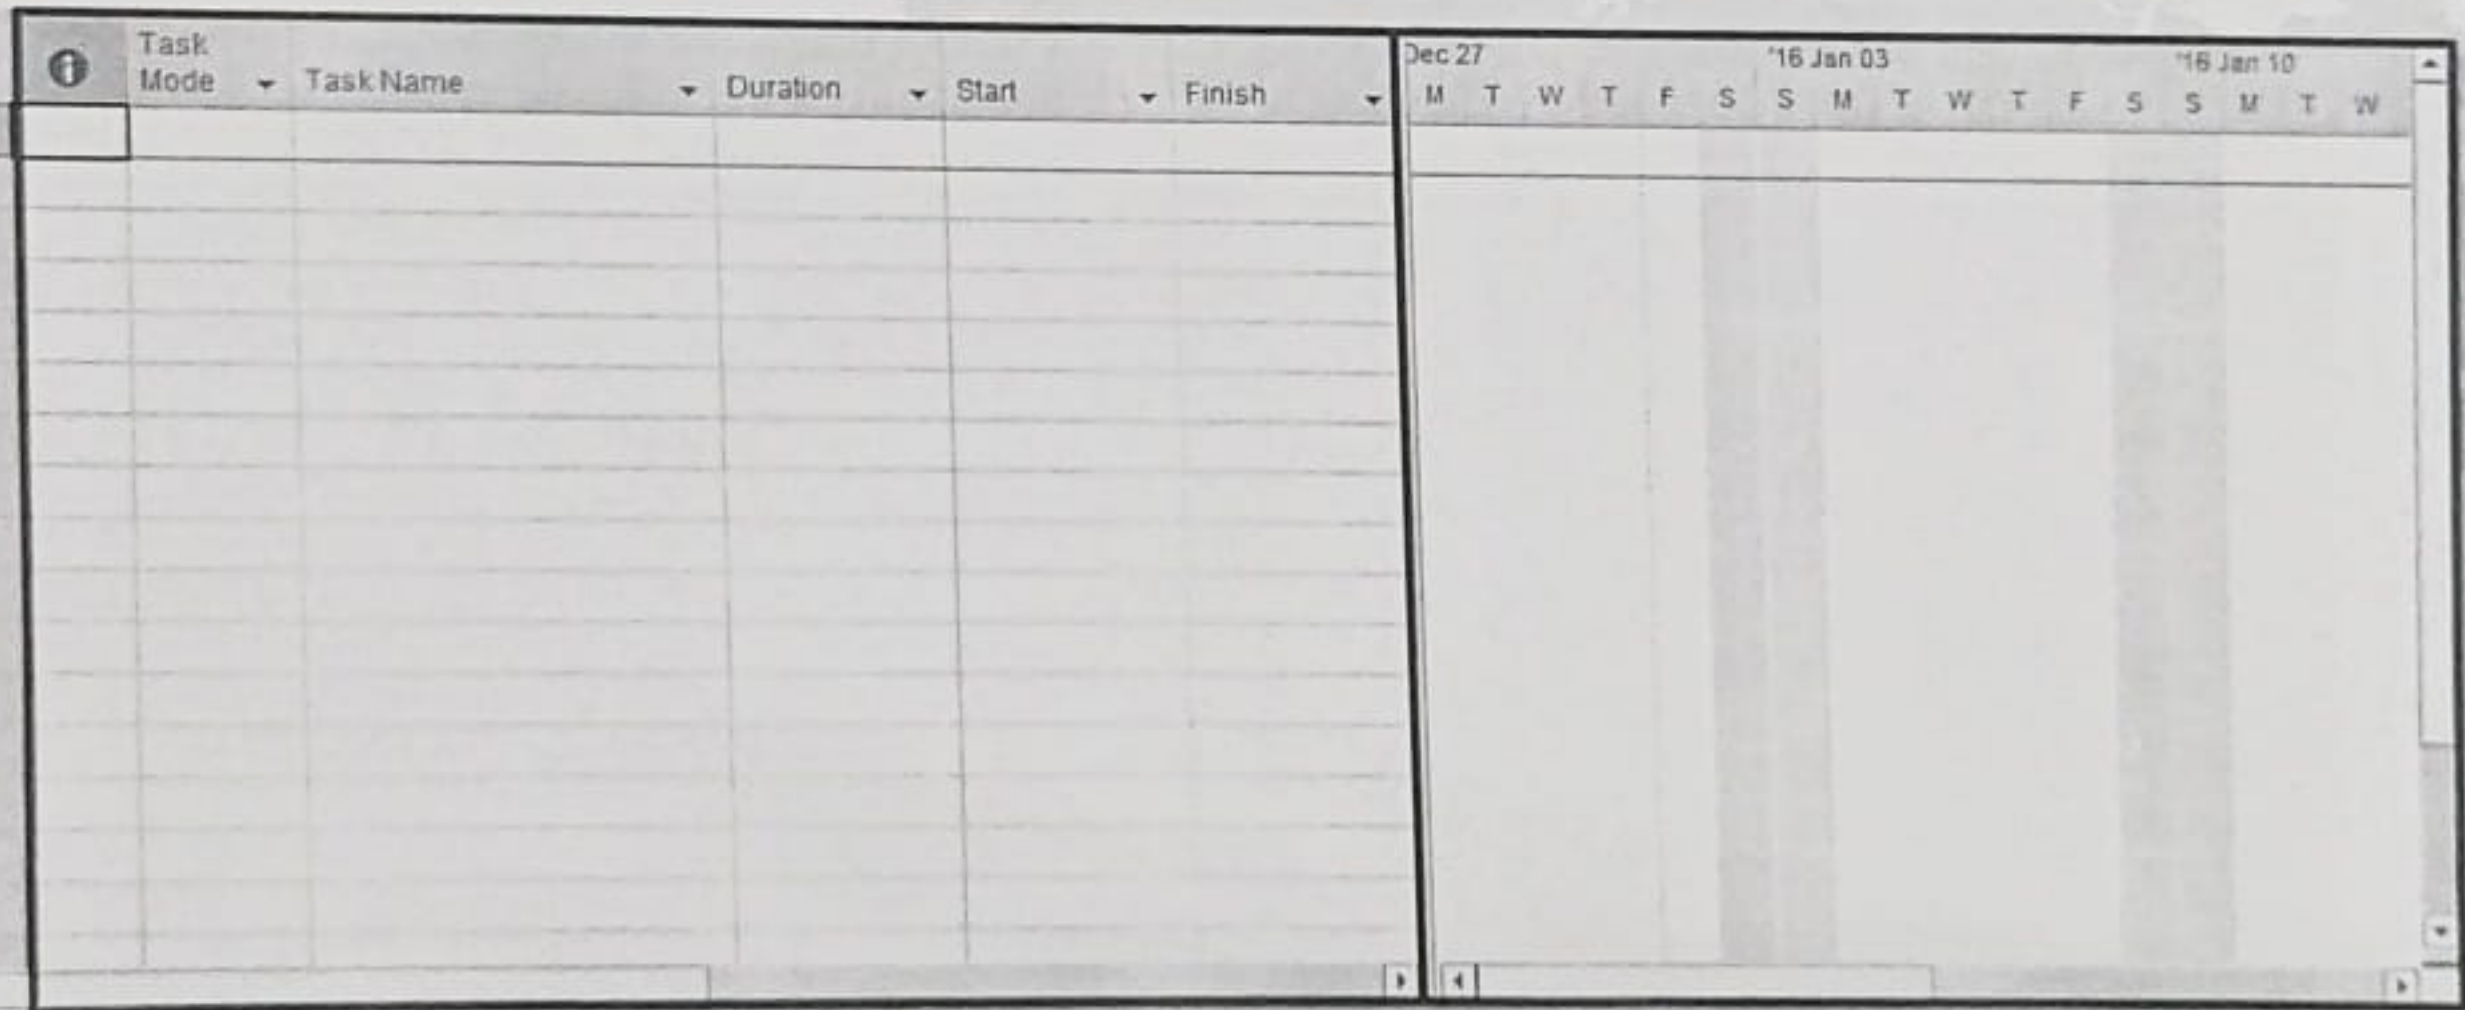

Task Relationships

TRACKING GANTT

| Task Name | Duration | Start | Finish | Predecessors |
|--|----------|--------------|--------------|--------------|
| Diamond Implementation Project | 0 days | Fri 16-01-01 | Fri 16-01-01 | |
| Project Preparation | | | | |
| 1st Project Kickoff meeting | 1 day | Fri 16-01-01 | Fri 16-01-01 | |
| Project Charter | 5 days | Mon 16-01-04 | Fri 16-01-08 | 3 |
| Org Structure | 3 days | Mon 16-01-04 | Wed 16-01-06 | 3 |
| BRD | 15 day | Thu 16-01-07 | Wed 16-01-27 | 5 |
| Gap Analysis RICEF | | | | |
| Finalise reporting requirements | | | | |
| Finalize Interface Requirements | | | | |
| Finalize Conversion Requirements | | | | |
| Finalize Enhancement Requirements | | | | |
| Finalize Forms Requirement | | | | |
| Finalize Workflow Requirements | | | | |
| Sign Off Project Charter | | | | |
| Business Blueprint | 18 day | Thu 16-01-14 | Mon 16-02-08 | 4 |
| 2nd Project Kickoff meeting | 1 day | Thu 16-01-14 | Thu 16-01-14 | 14 |
| BBP FICO Meetings | 10 day | Fri 16-01-15 | Fri 16-01-29 | 16 |
| BBP SD Meetings | 5 days | Fri 16-01-15 | Thu 16-01-21 | 16 |
| BBP MM Meetings | 5 days | Fri 16-01-15 | Thu 16-01-21 | 16 |
| BBP BI Meetings | 5 days | Fri 16-01-15 | Thu 16-01-21 | 16 |
| Business Blueprints Integration Workshop | 5 days | Mon 16-02-01 | Fri 16-02-05 | 17,18 |
| Sign Off Business Blueprints | 1 day | Mon 16-02-08 | Mon 16-02-08 | 21 |
| Realization | 40 day | Tue 16-02-09 | Mon 16-04-04 | |
| Project Team Status Meetings | 10 day | Tue 16-02-09 | Mon 16-02-22 | 22 |
| System Configuration | 30 day | Tue 16-02-23 | Mon 16-04-04 | 24 |
| Training for IIT scenarios | 20 day | Tue 16-03-07 | Mon 16-03-27 | 24 |


Task Dependency

From: Org Structure

To: BRD

Type: **Finish-to-Start (FS)** Lag: 0d

Delete OK Cancel

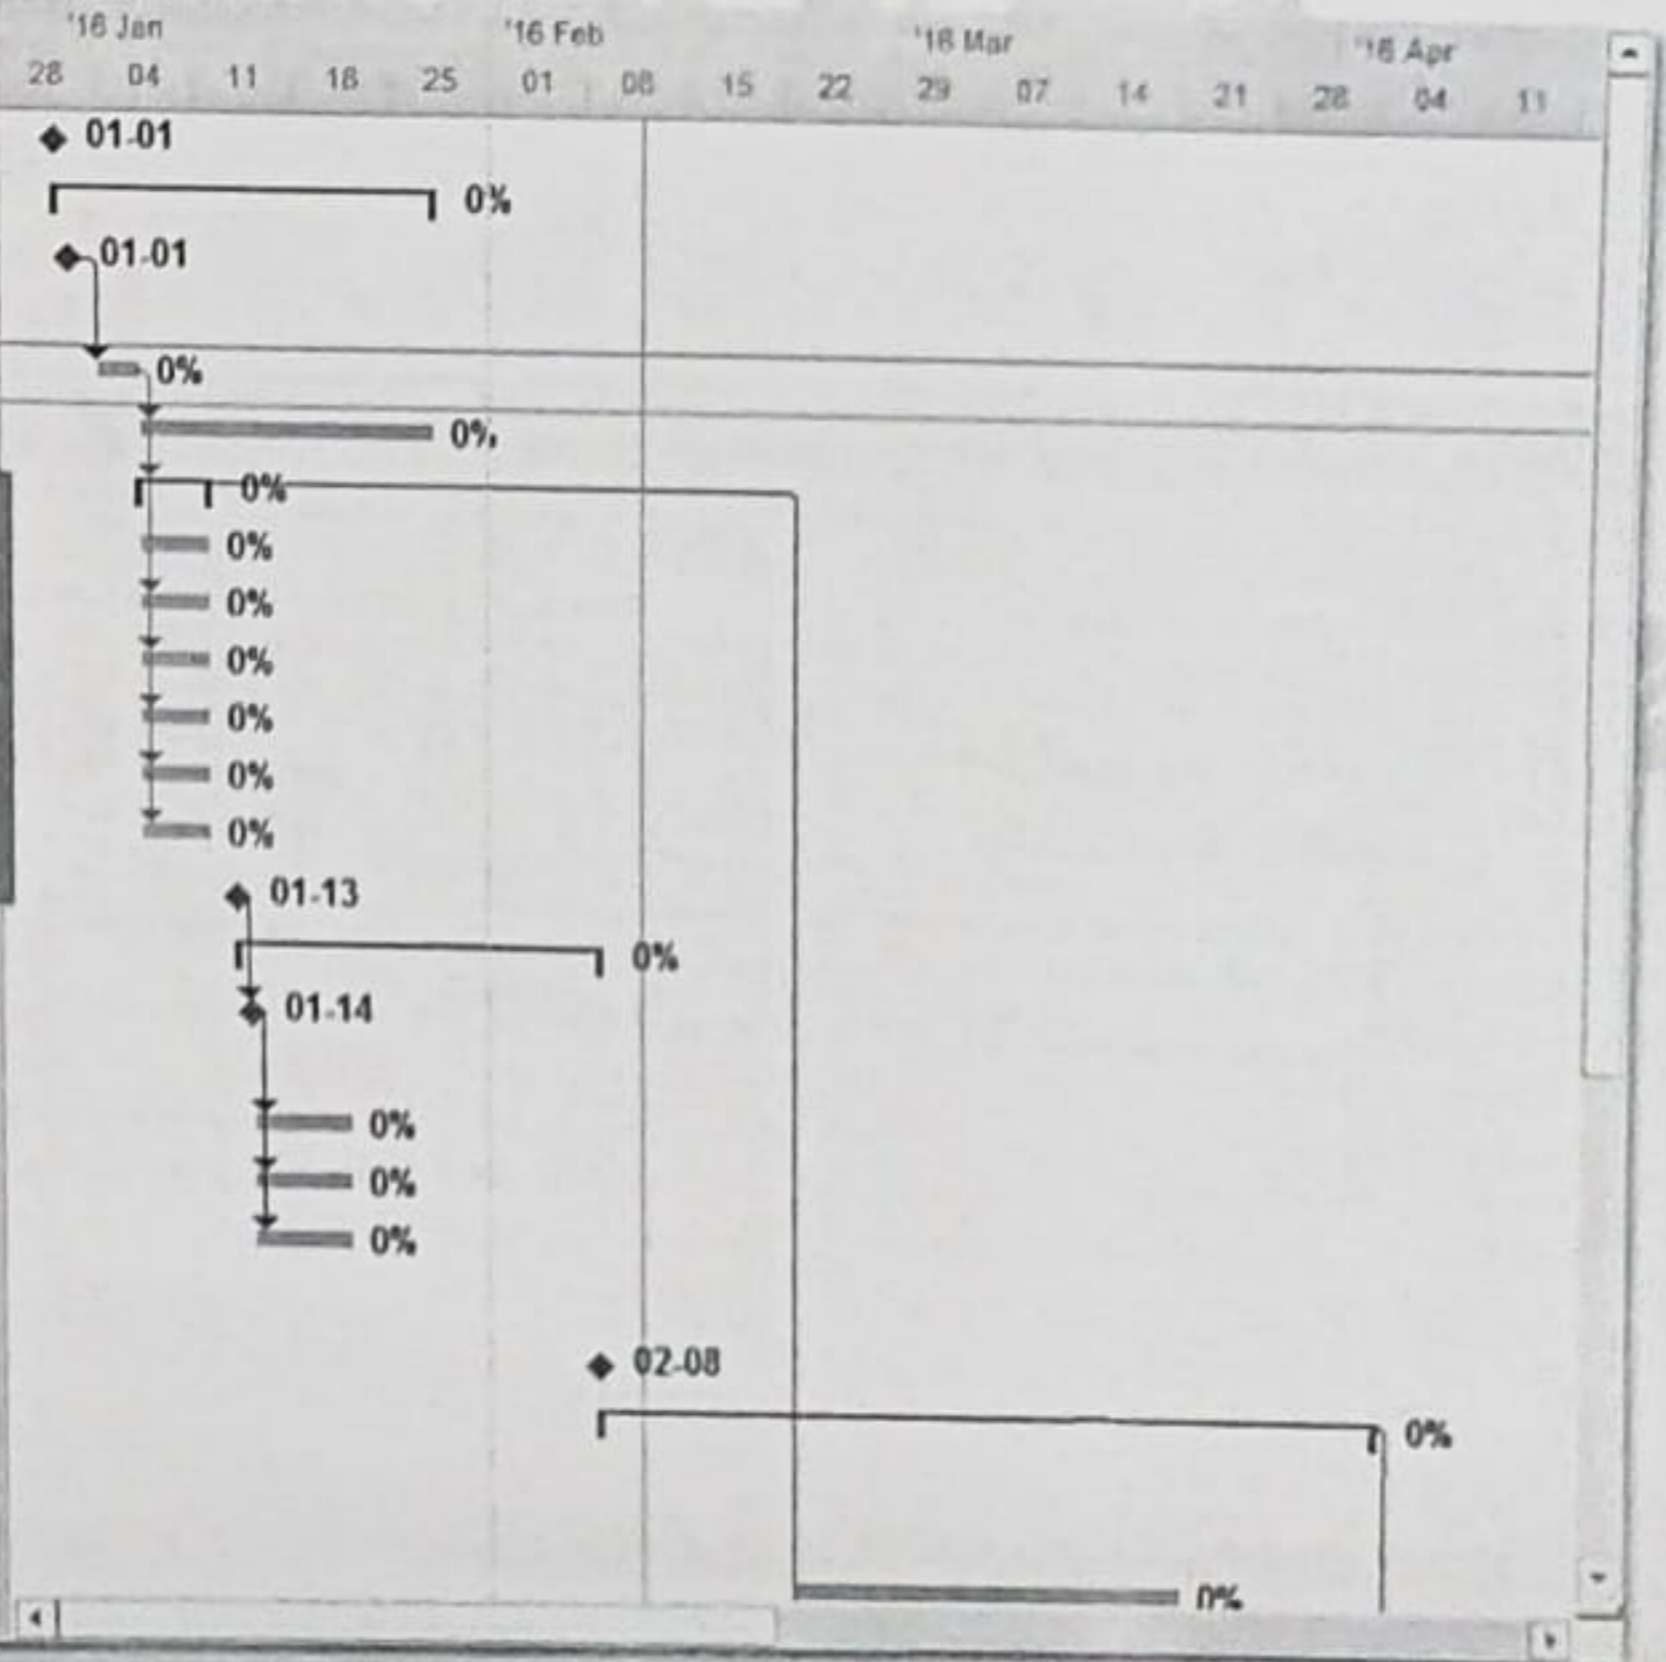

Task Information

Task Mode, Milestones, Summary, Sub Task, ...

| Task Mode | Task Name | Duration | Start | Finish |
|-----------|--|----------------|---------------------|---------------------|
| | Project Preparation | 19 days | Fri 16-01-01 | Wed 16-01-07 |
| | 1st Project Kickoff meeting | 1 day | Fri 16-01-01 | Fri 16-01-01 |
| | Project Charter | 5 days | Mon 16-01-04 | Fri 16-01-08 |
| | Org Structure | 3 days | Mon 16-01-04 | Thu 16-01-07 |
| | BRD | 15 days | Thu 16-01-07 | Wed 16-01-21 |
| | Gap Analysis RICEF | 3 days | Thu 16-01-07 | Mon 16-01-11 |
| | Finalise reporting requirement | 3 days | Thu 16-01-07 | Mon 16-01-11 |
| | Finalize Interface Requirement | 3 days | Thu 16-01-07 | Mon 16-01-11 |
| | Finalize Conversion Requirement | 3 days | Thu 16-01-07 | Mon 16-01-11 |
| | Finalize Enhancement Requirement | 3 days | Thu 16-01-07 | Mon 16-01-11 |
| | Finalize Forms Requirement | 3 days | Thu 16-01-07 | Mon 16-01-11 |
| | Finalize Workflow Requirements | 3 days | Thu 16-01-07 | Mon 16-01-11 |
| | Sign Off Project Charter | 3 days | Mon 16-01-11 | Wed 16-01-13 |
| | Business Blueprint | 18 days | Thu 16-01-14 | Mon 16-02-01 |
| | 2nd Project Kickoff meeting | 1 day | Thu 16-01-14 | Thu 16-01-14 |
| | BBP FICO Meetings | 10 days | Fri 16-01-15 | Fri 16-01-25 |
| | BBP SD Meetings | 5 days | Fri 16-01-15 | Thu 16-01-22 |
| | BBP MM Meetings | 5 days | Fri 16-01-15 | Thu 16-01-22 |
| | BBP BI Meetings | 5 days | Fri 16-01-15 | Thu 16-01-22 |
| | Business Blueprints Integration Workshop | 5 days | Mon 16-02-01 | Fri 16-02-05 |
| | Sign Off Business Blueprints | 1 day | Mon 16-02-08 | Mon 16-02-08 |
| | Realization | 40 days | Tue 16-02-09 | Mon 16-03-21 |
| | Project Team Status Meetings | 10 days | Tue 16-02-09 | Mon 16-02-22 |
| | System Configuration | 30 days | Tue 16-02-23 | Mon 16-04-04 |
| | Training for UT scenarios | 20 days | Tue 16-02-23 | Mon 16-03-21 |
| | RICEF Programs Development | 10 days | Tue 16-02-23 | Mon 16-03-07 |

Task Information

General | Predecessors | Resources | Advanced | Notes | Custom Fields

Task Information

General | Predecessors | Resources | Advanced | Notes | Custom Fields

Task Information

General | Predecessors | Resources | **Advanced** | Notes | Custom Fields

Name: Business Blueprints Integration Workshop Duration: 5 days Estimated

Constrain task

Deadline: NA

Constraint type: As Soon As Possible Constraint date: NA

Task type: Fixed Units Effort driven

Calendar: None Scheduling ignores resource calendars


WBS code: 3.6

Earned value method: % Complete

Mark task as milestone

Help OK Cancel

FS Finish-to-Start Relationship

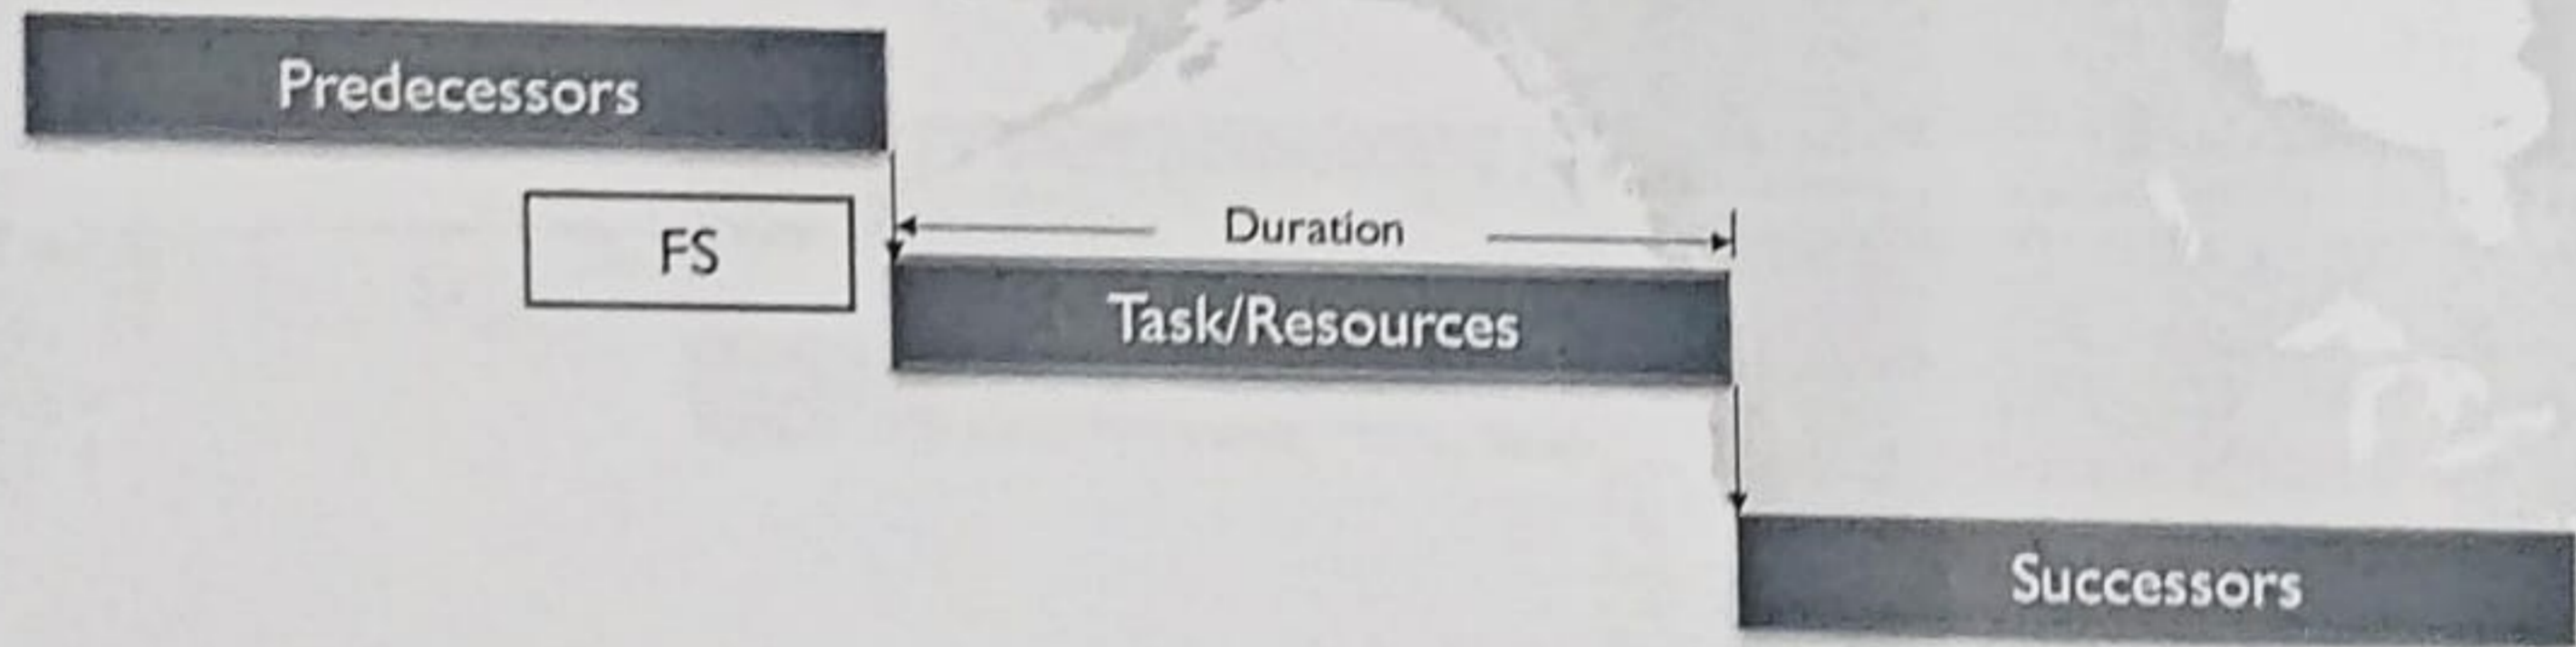

Creating Tasks Relationships

Note:

MS project will calculate dates based on the durations of the tasks, their relationships and the start date set for the project, however it is possible to change the starting date of a task (if necessary) By double clicking on a Task or milestone, and using the fields related to the dates (Start or Finish).

Task Information

General | Predecessors | Resources | Advanced | Notes | Custom Fields


Name: Business Blueprints Integration Workshop Duration: 5 days Estimated

Predecessors:


| ID | Task Name | Type | Lag |
|----|-------------------|-----------------------|-----|
| 17 | BBP FICO Meetings | Finish-to-Start (FS) | 0d |
| 18 | BBP SD Meetings | Finish-to-Start (FS) | 0d |
| 19 | BBP MM Meetings | Start-to-Start (SS) | 0d |
| 20 | BBP BI Meetings | Finish-to-Finish (FF) | 0d |
| | | Start-to-Finish (SF) | 0d |
| | | (None) | |

Help OK Cancel


FF Finish-to-Finish Relationship

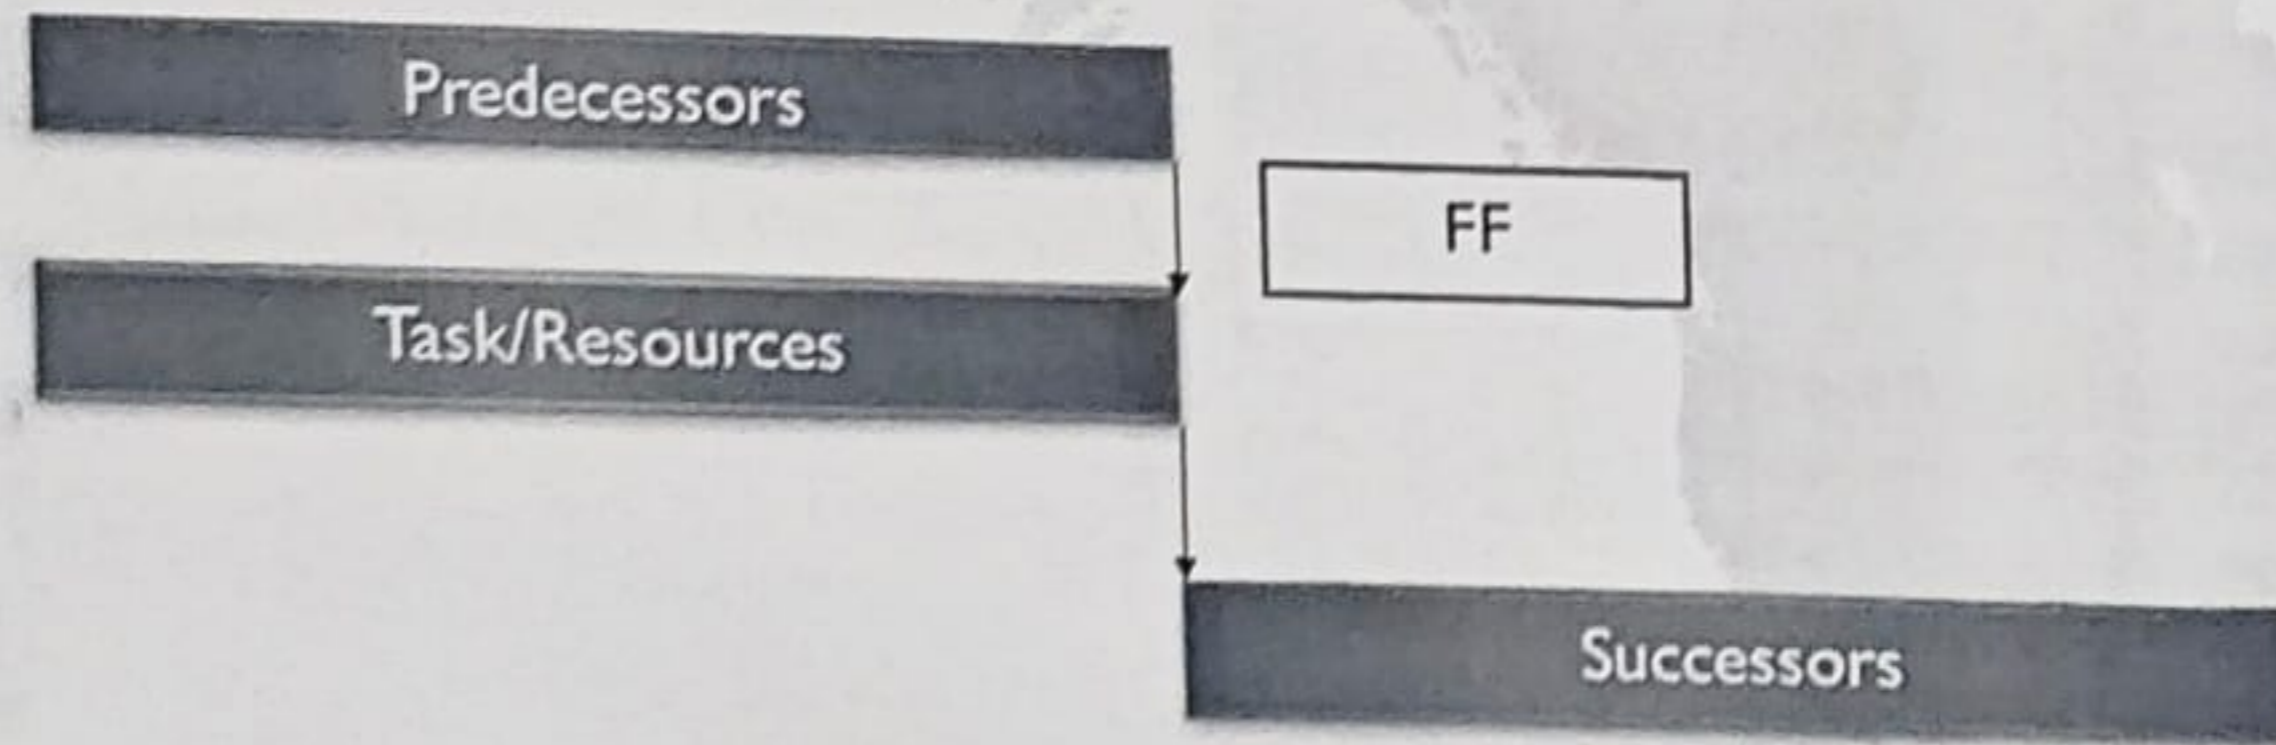


SS Start-to-Start Relationship

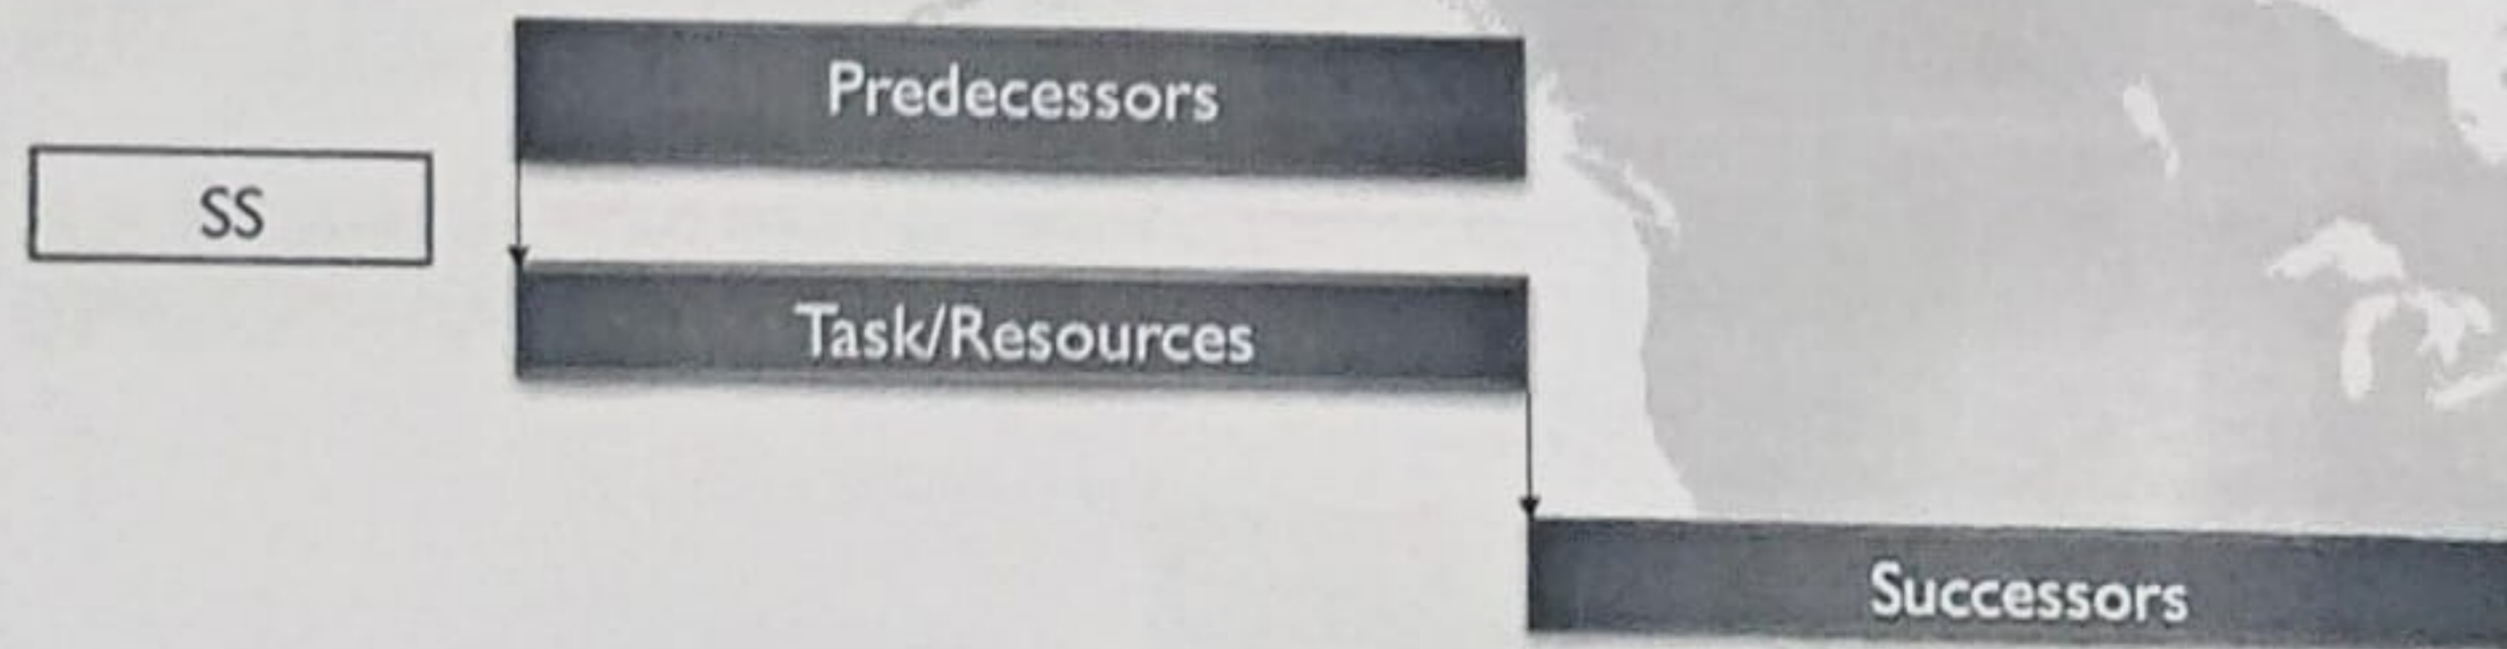


Lag

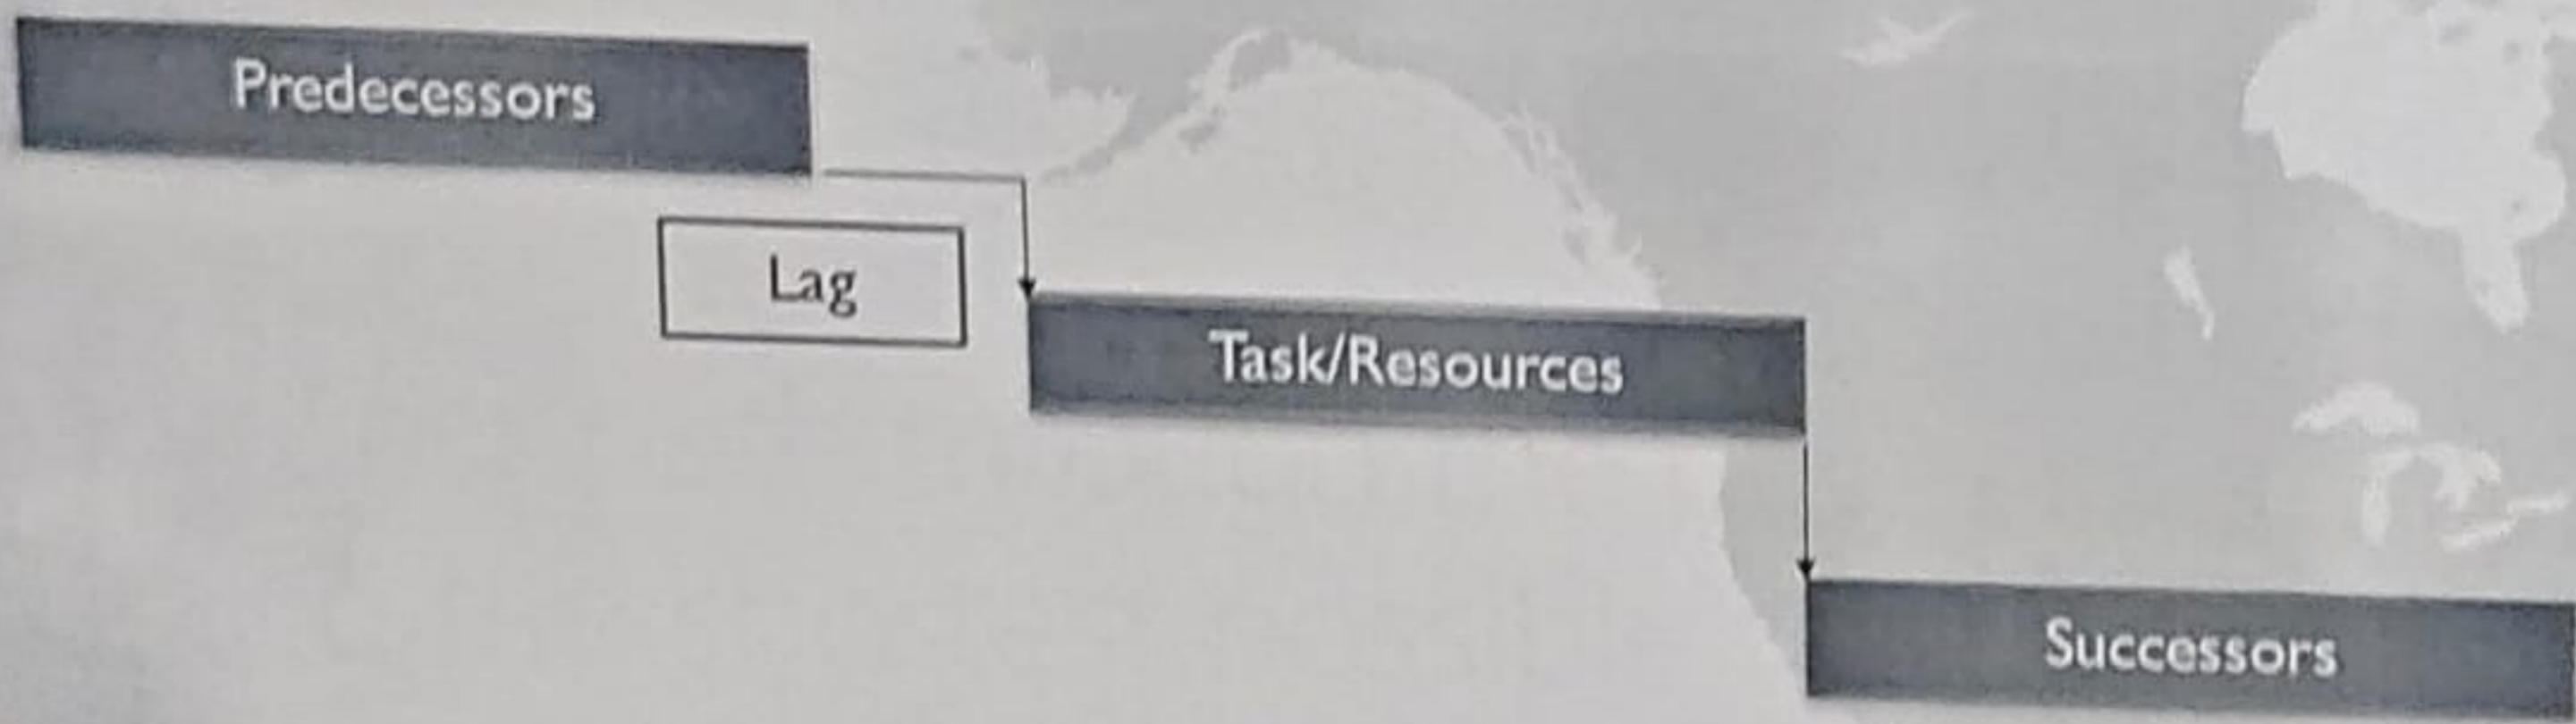


Overlap

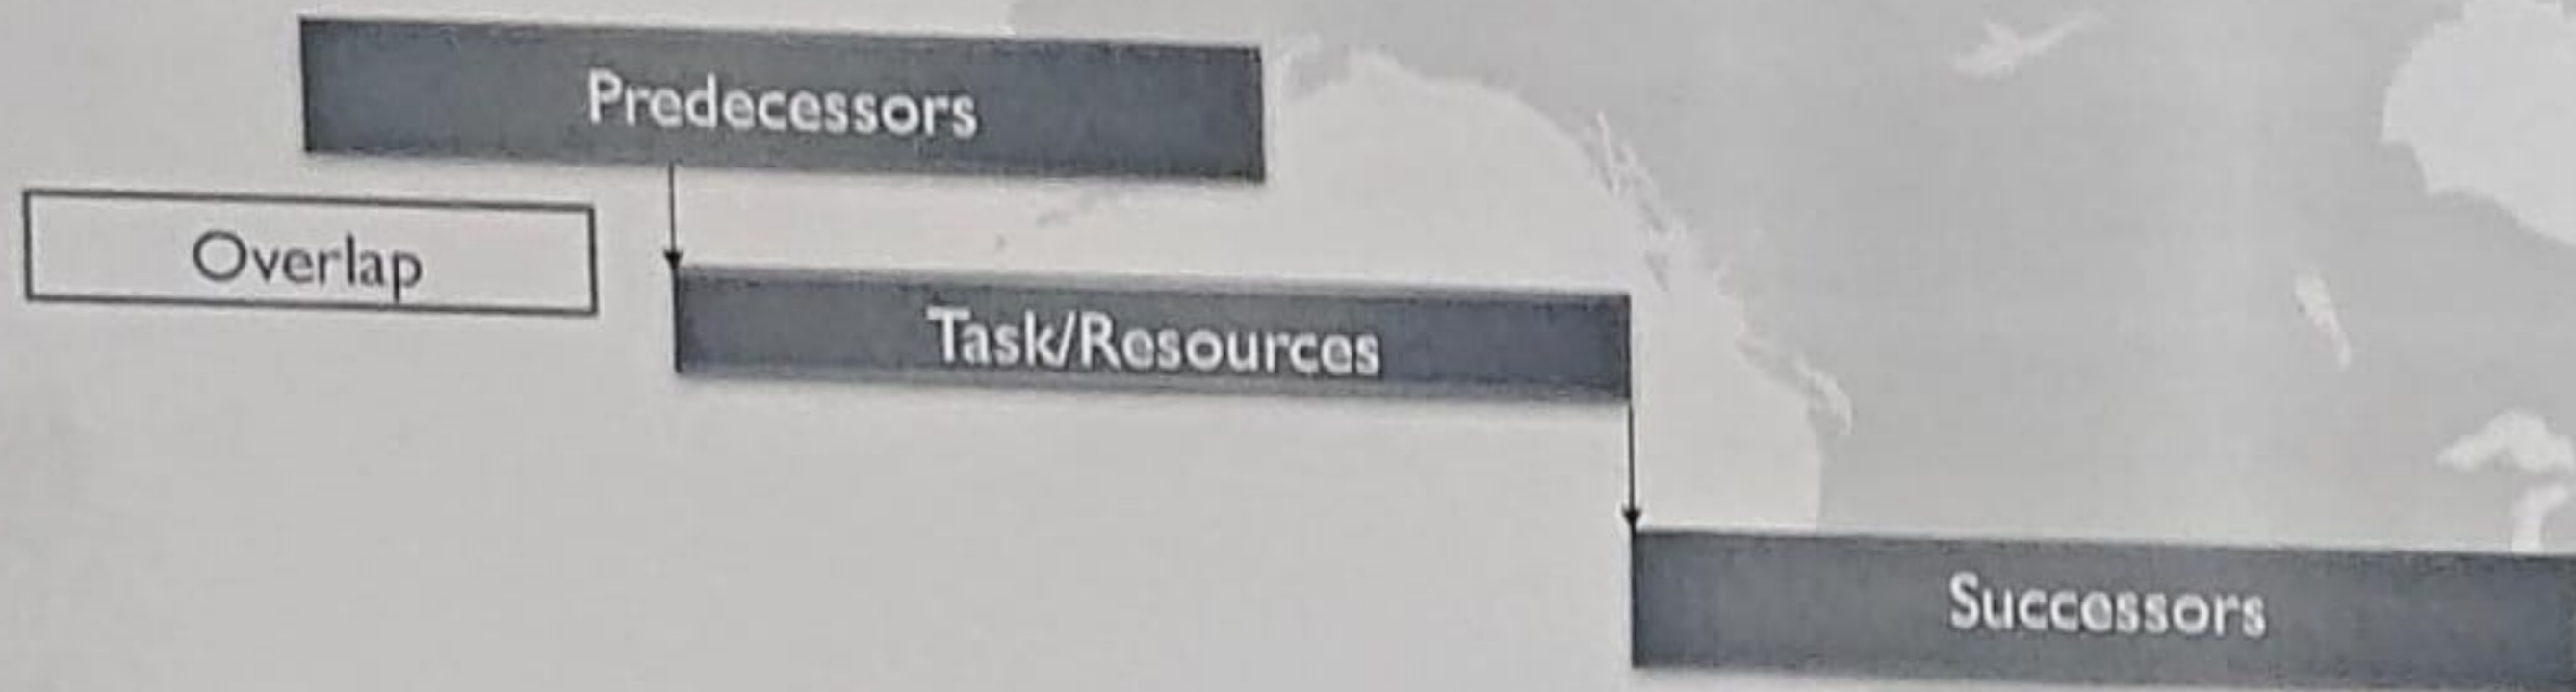

SF Start-to-Finish Relationship

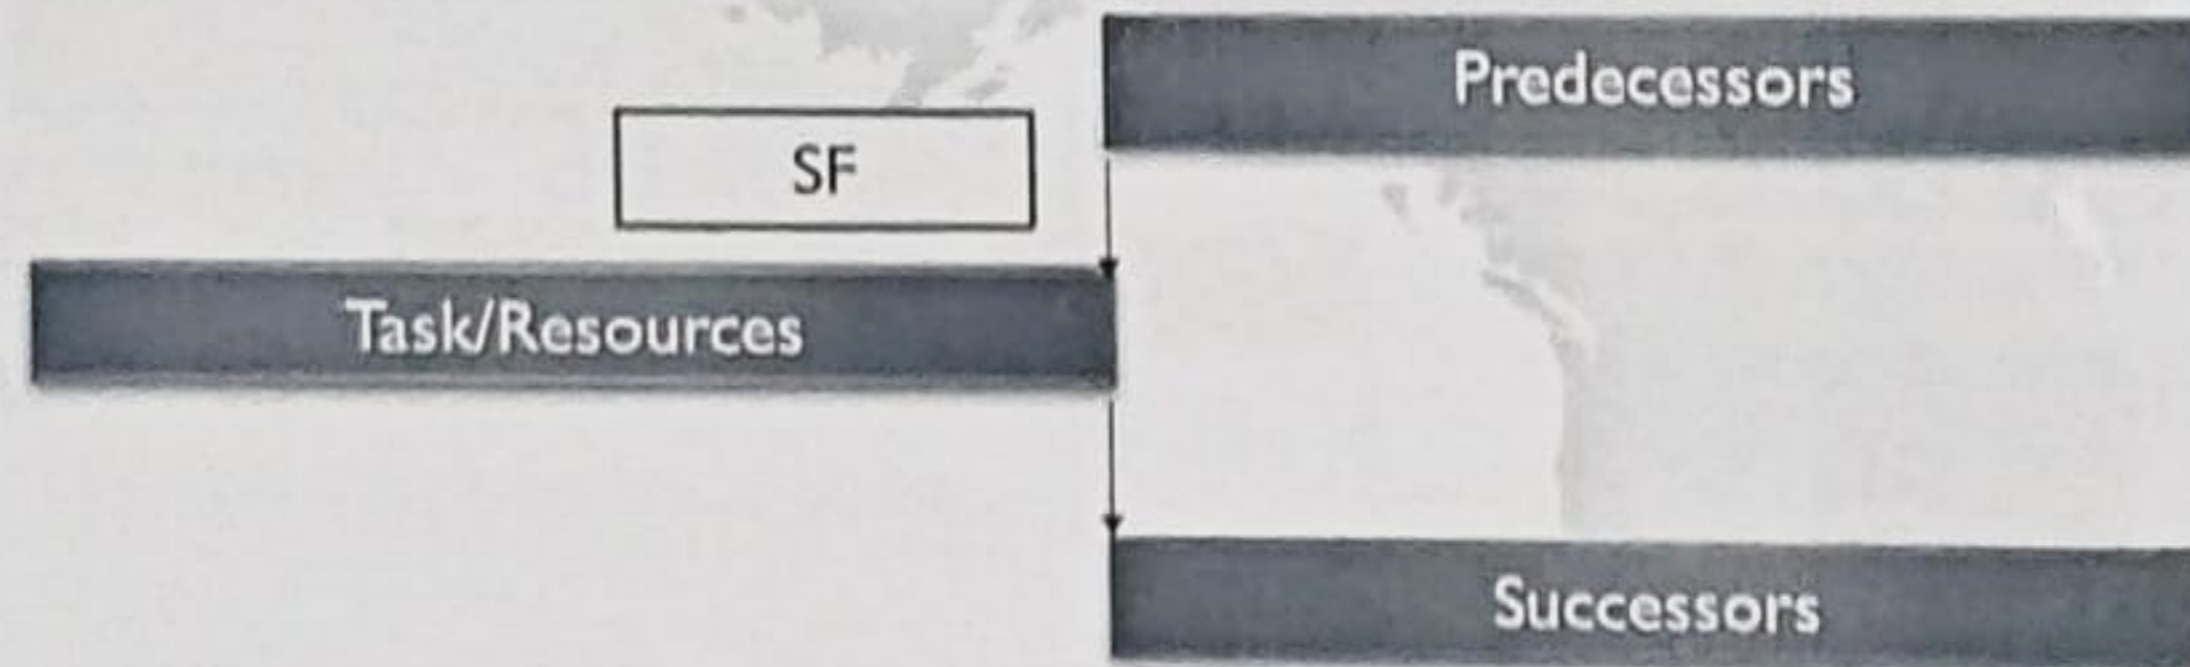

Showing Critical Path

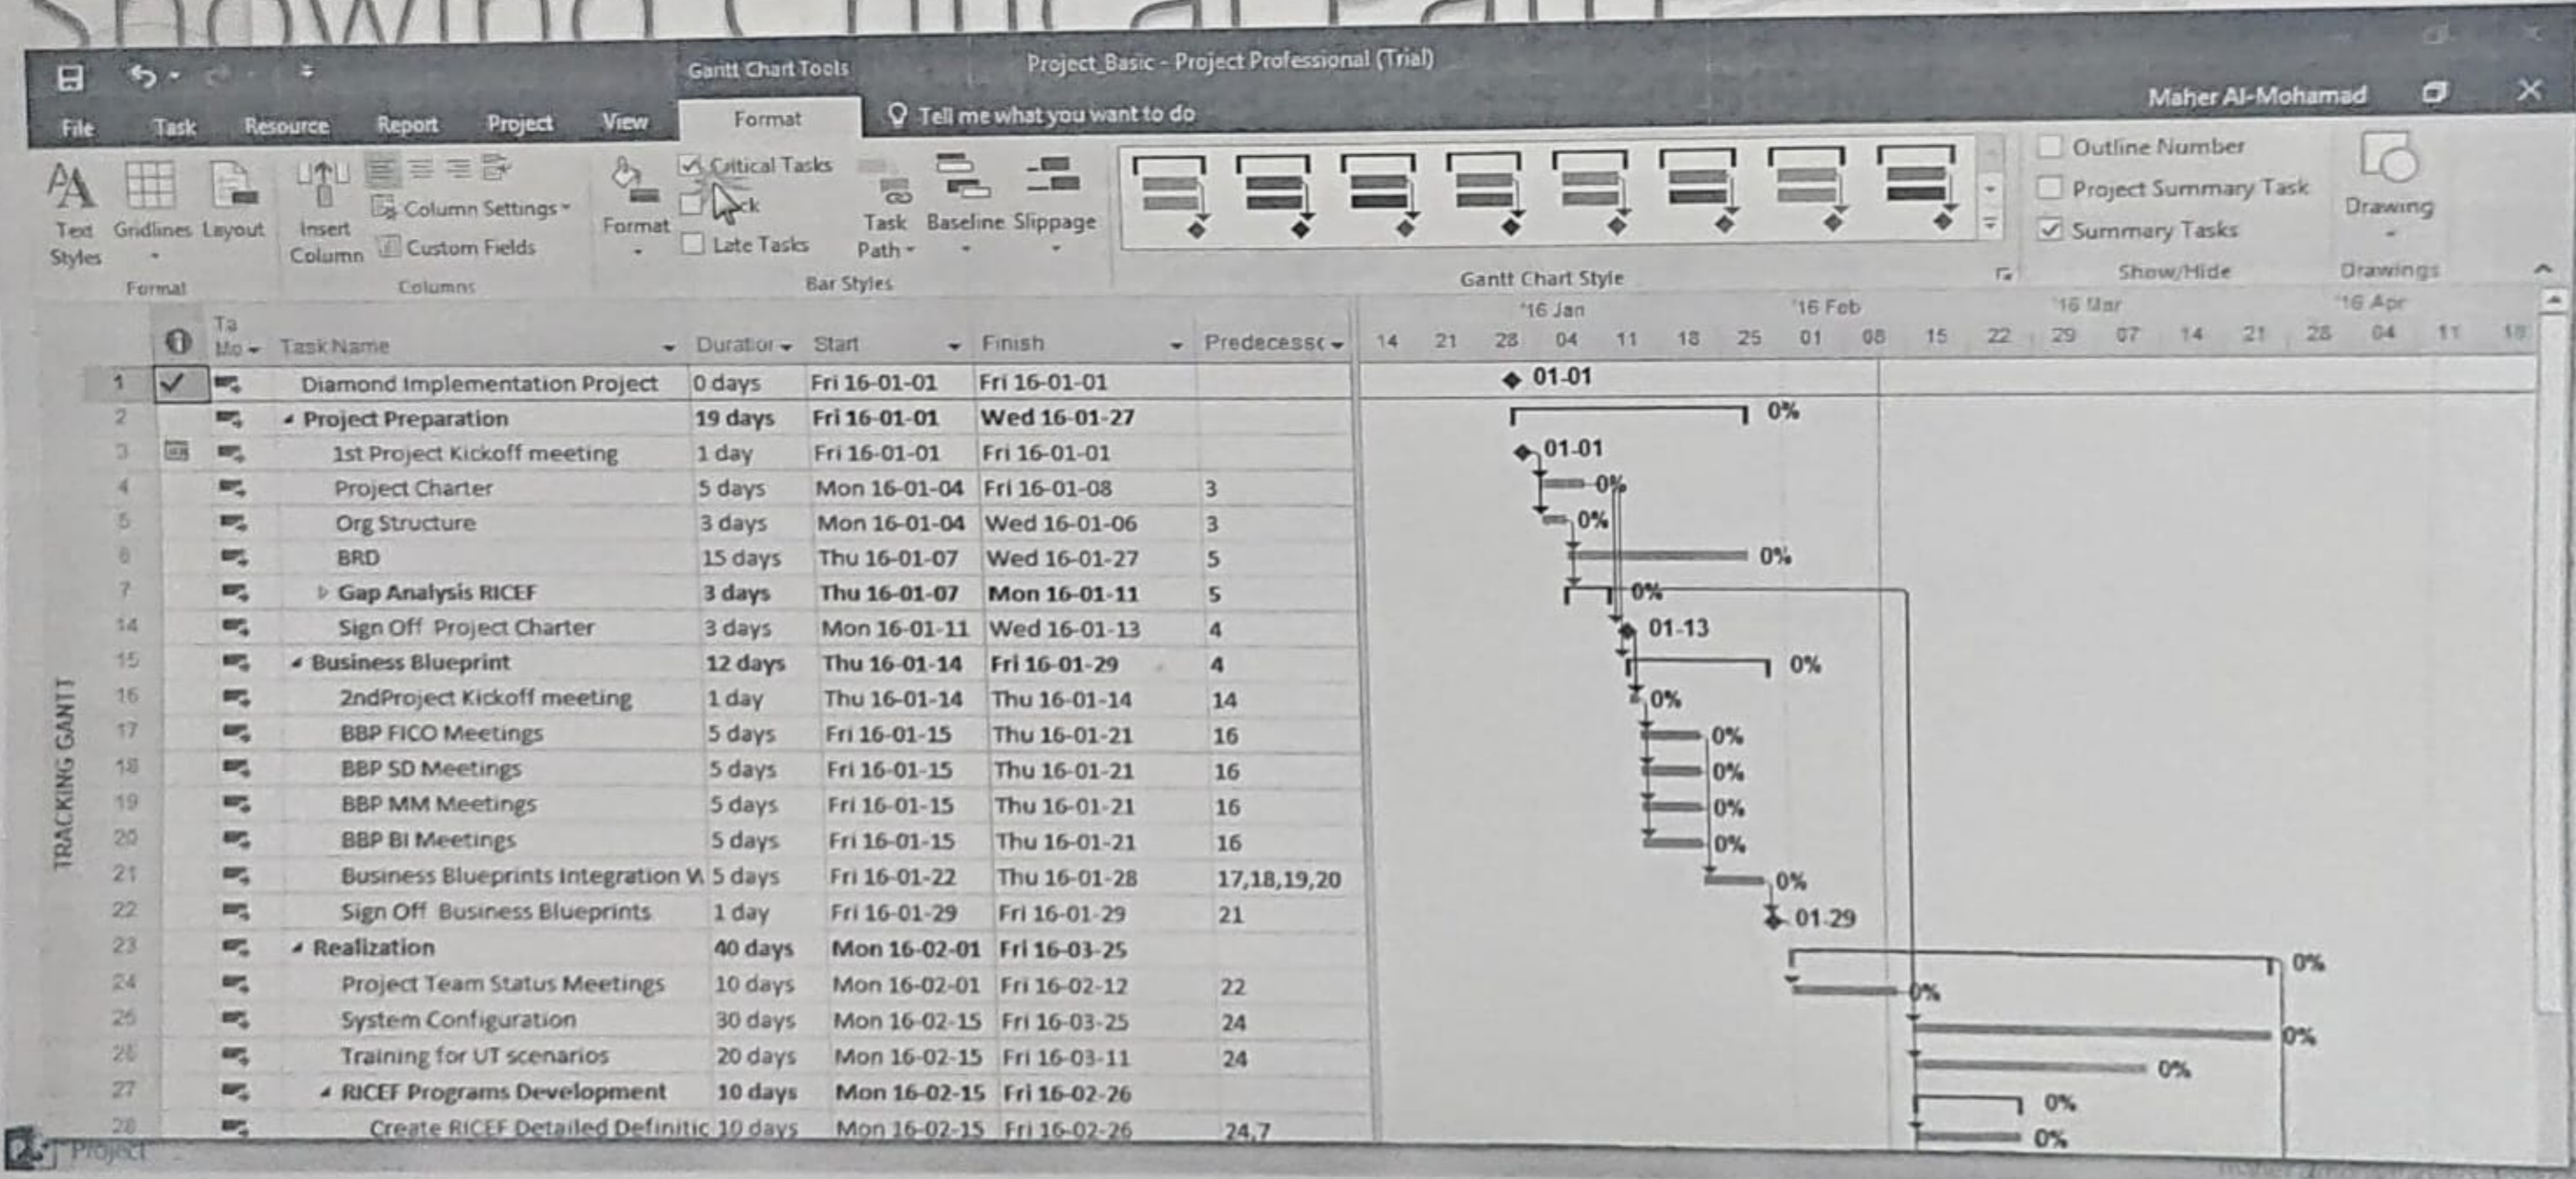

Project Statistics

Project_Basic - Project Professional (Trial)

Maheer Al-Mohamad

- ←
- Info
- New
- Open
- Save
- Save As
- Print
- Share
- Export
- Close
- Account
- Options

Info

Project_Basic

Desktop



Project Web App Accounts
You're not connected to Project Web App



Organize Global Template
Move views, reports, and other elements between project files and the global template.

Project Information

- Advanced Properties**
View advanced and custom properties of this project.
- Project Statistics**
See key statistics related to your project.

Last Modified: Today
Project Calendar
Priority

| | Start | | Finish | |
|-------------------|--------------|----------|--------------|--|
| Current | Fri 16-01-01 | | Tue 16-04-12 | |
| Baseline | NA | | NA | |
| Actual | Fri 16-01-01 | | NA | |
| Variance | 0d | | 0d | |
| | Duration | Work | Cost | |
| Current | 73d | 0h | \$0.00 | |
| Baseline | 0d | 0h | \$0.00 | |
| Actual | 0d | 0h | \$0.00 | |
| Remaining | 73d | 0h | \$0.00 | |
| Percent complete: | | | | |
| Duration: 0% | | Work: 0% | | |

Assigning Resources to Tasks

1. Assign Resources Using Task List Resources Name Column

| Task ID | Task Name | Duration | Start | Finish | Predecessors | Resource Names | Remaining Work |
|---------|-----------------------------------|----------|--------------|--------------|--------------|---|----------------|
| 1 | Diamond Implementation Project | 0 days | Fri 16-01-01 | Fri 16-01-01 | | | |
| 2 | Project Preparation | 19 days | Fri 16-01-01 | Wed 16-01-27 | | | |
| 3 | 1st Project Kickoff meeting | 1 day | Fri 16-01-01 | Fri 16-01-01 | | | 0 hrs |
| 4 | Project Charter | 5 days | Mon 16-01-04 | Fri 16-01-08 | 3 | Abiodun Giwa[60%], Amjad Al Hamadneh[70%], Mathew Neduvamkunnil[70%], R... | 29.6 hrs |
| 5 | Org Structure | 3 days | Mon 16-01-04 | Wed 16-01-06 | 3 | <input checked="" type="checkbox"/> Abiodun Giwa <input checked="" type="checkbox"/> Amjad Al Hamadneh <input type="checkbox"/> Bhavik Joshi <input type="checkbox"/> Maher Al Mohamed <input checked="" type="checkbox"/> Mathew Neduvamkunnil <input type="checkbox"/> Nafees Ahmed <input checked="" type="checkbox"/> Rajeer Kumar <input type="checkbox"/> Rana Izhar Ul Haq <input type="checkbox"/> Sadim Rasheed <input checked="" type="checkbox"/> Sunil Singh <input type="checkbox"/> Venancio Mostacho <input type="checkbox"/> Wesam Al Henani | 29.6 hrs |
| 6 | BRD | 15 days | Thu 16-01-07 | Wed 16-01-27 | 5 | | 0 hrs |
| 7 | Gap Analysis RICEF | 3 days | Thu 16-01-07 | Mon 16-01-11 | 5 | | 0 hrs |
| 8 | Sign Off Project Charter | 3 days | Mon 16-01-11 | Wed 16-01-13 | 4 | | 0 hrs |
| 9 | Business Blueprint | 12 days | Thu 16-01-14 | Fri 16-01-29 | 4 | | 0 hrs |
| 10 | 2nd Project Kickoff meeting | 1 day | Thu 16-01-14 | Thu 16-01-14 | 14 | | 0 hrs |
| 11 | BBP FICO Meetings | 5 days | Fri 16-01-15 | Thu 16-01-21 | 16 | | 0 hrs |
| 12 | BBP SD Meetings | 5 days | Fri 16-01-15 | Thu 16-01-21 | 16 | | 0 hrs |
| 13 | BBP MM Meetings | 5 days | Fri 16-01-15 | Thu 16-01-21 | 16 | | 0 hrs |
| 14 | BBP BI Meetings | 5 days | Fri 16-01-15 | Thu 16-01-21 | 16 | | 0 hrs |
| 15 | Business Blueprints Integration W | 5 days | Fri 16-01-22 | Thu 16-01-28 | 17,18,19,20 | | 0 hrs |
| 16 | Sign Off Business Blueprints | 1 day | Fri 16-01-29 | Fri 16-01-29 | 21 | | 0 hrs |
| 17 | Realization | 40 days | Mon 16-02-01 | Fri 16-03-25 | | | 0 hrs |
| 18 | Project Team Status Meetings | 10 days | Mon 16-02-01 | Fri 16-02-12 | 22 | | 0 hrs |
| 19 | System Configuration | 30 days | Mon 16-02-15 | Fri 16-03-25 | 24 | | 0 hrs |
| 20 | Training for UT scenarios | 20 days | Mon 16-02-15 | Fri 16-03-11 | 24 | | 0 hrs |
| 21 | RICEF Programs Development | 10 days | Mon 16-02-15 | Fri 16-02-26 | | | 0 hrs |
| 22 | Create RICEF Detailed Definitic | 10 days | Mon 16-02-15 | Fri 16-02-26 | 24,7 | | 0 hrs |
| 23 | Create RICEF Programs | 10 days | Mon 16-02-15 | Fri 16-02-26 | 24,7 | | 0 hrs |
| 24 | Test and Review RICEF Program | 10 days | Mon 16-02-15 | Fri 16-02-26 | 24,7 | | 0 hrs |

Working with Resources List

You can use the Resource Sheet to create a list of the people, equipment, and material resources.

| | Resource Name | Type | Material Label | Initials | Group | Max | Std Rate | OM Rate | Cost/Use | Accrue At | Base | Code | Add New Column |
|----|----------------------|------|----------------|----------|-------|------|-------------|-------------|----------|-----------|----------|------|----------------|
| 1 | Rajeev Kumar | Work | | R | PM | 70% | \$100.00/hr | \$175.00/hr | \$0.00 | Prorated | Standard | | |
| 2 | Maher Al Mohamad | Work | | M | FICO | 80% | \$50.00/hr | \$75.00/hr | \$0.00 | Prorated | Standard | | |
| 3 | Mathew Neduvamkunnil | Work | | M | SD | 70% | \$70.00/hr | \$100.00/hr | \$0.00 | Prorated | Standard | | |
| 4 | Sadim Rasheed | Work | | S | MM | 50% | \$50.00/hr | \$75.00/hr | \$0.00 | Prorated | Standard | | |
| 5 | Amjad Al Hamadneh | Work | | A | FICO | 70% | \$50.00/hr | \$75.00/hr | \$0.00 | Prorated | Standard | | |
| 6 | Rana Izhar Ul Haq | Work | | R | BI | 80% | \$50.00/hr | \$75.00/hr | \$0.00 | Prorated | Standard | | |
| 7 | Wesam Al Henani | Work | | W | FICO | 80% | \$50.00/hr | \$75.00/hr | \$0.00 | Prorated | Standard | | |
| 8 | Venancio Mostacho | Work | | V | ABAP | 100% | \$70.00/hr | \$100.00/hr | \$0.00 | Prorated | Standard | | |
| 9 | Abiodun Giwa | Work | | A | SD | 60% | \$70.00/hr | \$100.00/hr | \$0.00 | Prorated | Standard | | |
| 10 | Bhavik Joshi | Work | | B | FICO | 100% | \$50.00/hr | \$75.00/hr | \$0.00 | Prorated | Standard | | |
| 11 | Sunil Singh | Work | | S | MM | 100% | \$50.00/hr | \$75.00/hr | \$0.00 | Prorated | Standard | | |
| 12 | Nafees Ahmed | Work | | N | MM | 50% | \$50.00/hr | \$75.00/hr | \$0.00 | Prorated | Standard | | |

The Critical Path

CP is the flow of tasks, of which, a delay in any one of these tasks will cause a delay to the project.

It is the longest path through the project network diagram and the shortest possible time to complete the project.

Task Usage View

| | | | | 2016 January | | | | | | | | | | | |
|-----------|------------------------|-----------|----------|--------------|----|-------|-------|--------|-------|--------|-------|-------|-------|--|--|
| Task Mode | Task Name | Work | Duration | Details | 27 | 30 | 02 | 05 | 08 | 11 | 14 | 17 | 20 | | |
| ✓ | Diamond Implementatio | 0 hrs | 0 days | Work | | | | | | | | | | | |
| | Project Preparation | 465.6 hrs | 14 days | Work | | 29.6h | 27.2h | 127.2h | 72.8h | 112.8h | 38.4h | 38.4h | 19.2h | | |
| | 1st Project Kickoff me | 29.6 hrs | 1 day | Work | | 29.6h | | | | | | | | | |
| | Rajeev Kumar | 5.6 hrs | | Work | | 5.6h | | | | | | | | | |
| | Mathew Neduvann | 5.6 hrs | | Work | | 5.6h | | | | | | | | | |
| | Amjad Al Hamadn | 5.6 hrs | | Work | | 5.6h | | | | | | | | | |
| | Abiodun Giwa | 4.8 hrs | | Work | | 4.8h | | | | | | | | | |
| | Sunil singh | 8 hrs | | Work | | 8h | | | | | | | | | |
| | Project Charter | 76 hrs | 5 days | Work | | | 15.2h | 45.6h | 15.2h | | | | | | |
| | Maher Al Mohamc | 32 hrs | | Work | | | 6.4h | 19.2h | 6.4h | | | | | | |
| | Sadim Rasheed | 20 hrs | | Work | | | 4h | 12h | 4h | | | | | | |
| | Abiodun Giwa | 24 hrs | | Work | | | 4.8h | 14.4h | 4.8h | | | | | | |
| | Org Structure | 36 hrs | 3 days | Work | | | 12h | 24h | | | | | | | |
| | Rajeev Kumar | 16.8 hrs | | Work | | | 5.6h | 11.2h | | | | | | | |
| | Wesam Al Henani | 19.2 hrs | | Work | | | 6.4h | 12.8h | | | | | | | |
| | BRD | 192 hrs | 10 days | Work | | | | 19.2h | 19.2h | 57.6h | 38.4h | 38.4h | 19.2h | | |
| | Mathew Neduvann | 56 hrs | | Work | | | | 5.6h | 5.6h | 16.8h | 11.2h | 11.2h | 5.6h | | |
| | Amjad Al Hamadn | 56 hrs | | Work | | | | 5.6h | 5.6h | 16.8h | 11.2h | 11.2h | 5.6h | | |
| | Sunil singh | 80 hrs | | Work | | | | 8h | 8h | 24h | 16h | 16h | 8h | | |
| | Gap Analysis RICEF | 115.2 hrs | 3 days | Work | | | | 38.4h | 38.4h | 38.4h | | | | | |
| | Finalize reporting r | 19.2 hrs | 3 days | Work | | | | 6.4h | 6.4h | 6.4h | | | | | |
| | Wesam Al Hena | 19.2 hrs | | Work | | | | 6.4h | 6.4h | 6.4h | | | | | |
| | Finalize Interface R | 24 hrs | 3 days | Work | | | | 8h | 8h | 8h | | | | | |
| | Bhavik Jashi | 24 hrs | | Work | | | | 8h | 8h | 8h | | | | | |
| | Fnalize Conversion | 19.2 hrs | 3 days | Work | | | | 6.4h | 6.4h | 6.4h | | | | | |
| | Rana Izhar Ul H | 19.2 hrs | | Work | | | | 6.4h | 6.4h | 6.4h | | | | | |
| | Finalize Enhanceme | 24 hrs | 3 days | Work | | | | 8h | 8h | 8h | | | | | |
| | Venancio Mostc | 24 hrs | | Work | | | | 8h | 8h | 8h | | | | | |
| | Finalize Forms Reqt | 12 hrs | 3 days | Work | | | | 4h | 4h | 4h | | | | | |
| | Nafees Ahmed | 12 hrs | | Work | | | | 4h | 4h | 4h | | | | | |

TASK USAGE

Updated

- ←
- Info
- New
- Open
- Save
- Save As
- Print
- Share
- Export
- Close
- Account
- Options

Project_Basic - Project Professional (Trial)

Mahe Al-Mohamad

Info


Project_Basic

Desktop



Project Web App Accounts

You're not connected to Project Web App



Organize Global Template

Move views, reports, and other elements between project files and the global template.

Project Information

Advanced Properties
View advanced and custom properties of this project.

Project Statistics
See key statistics related to your project.

Last Modified: Today

Project Calendar

Priority

Project Statistics for 'Project_Basic'

| | Start | | Finish | |
|-----------|----------|--------------|--------------|--------------|
| Current | | Fri 16-01-01 | | Fri 16-05-13 |
| Baseline | | NA | | NA |
| Actual | | Fri 16-01-01 | | NA |
| Variance | | 0d | | 0d |
| | Duration | Work | Cost | |
| Current | 96d | 4,915.2h | \$284,328.00 | |
| Baseline | 0d | 0h | \$0.00 | |
| Actual | 0d | 0h | \$0.00 | |
| Remaining | 96d | 4,915.2h | \$284,328.00 | |


Percent complete:

Duration: 0%

Work: 0%

Close

Resources

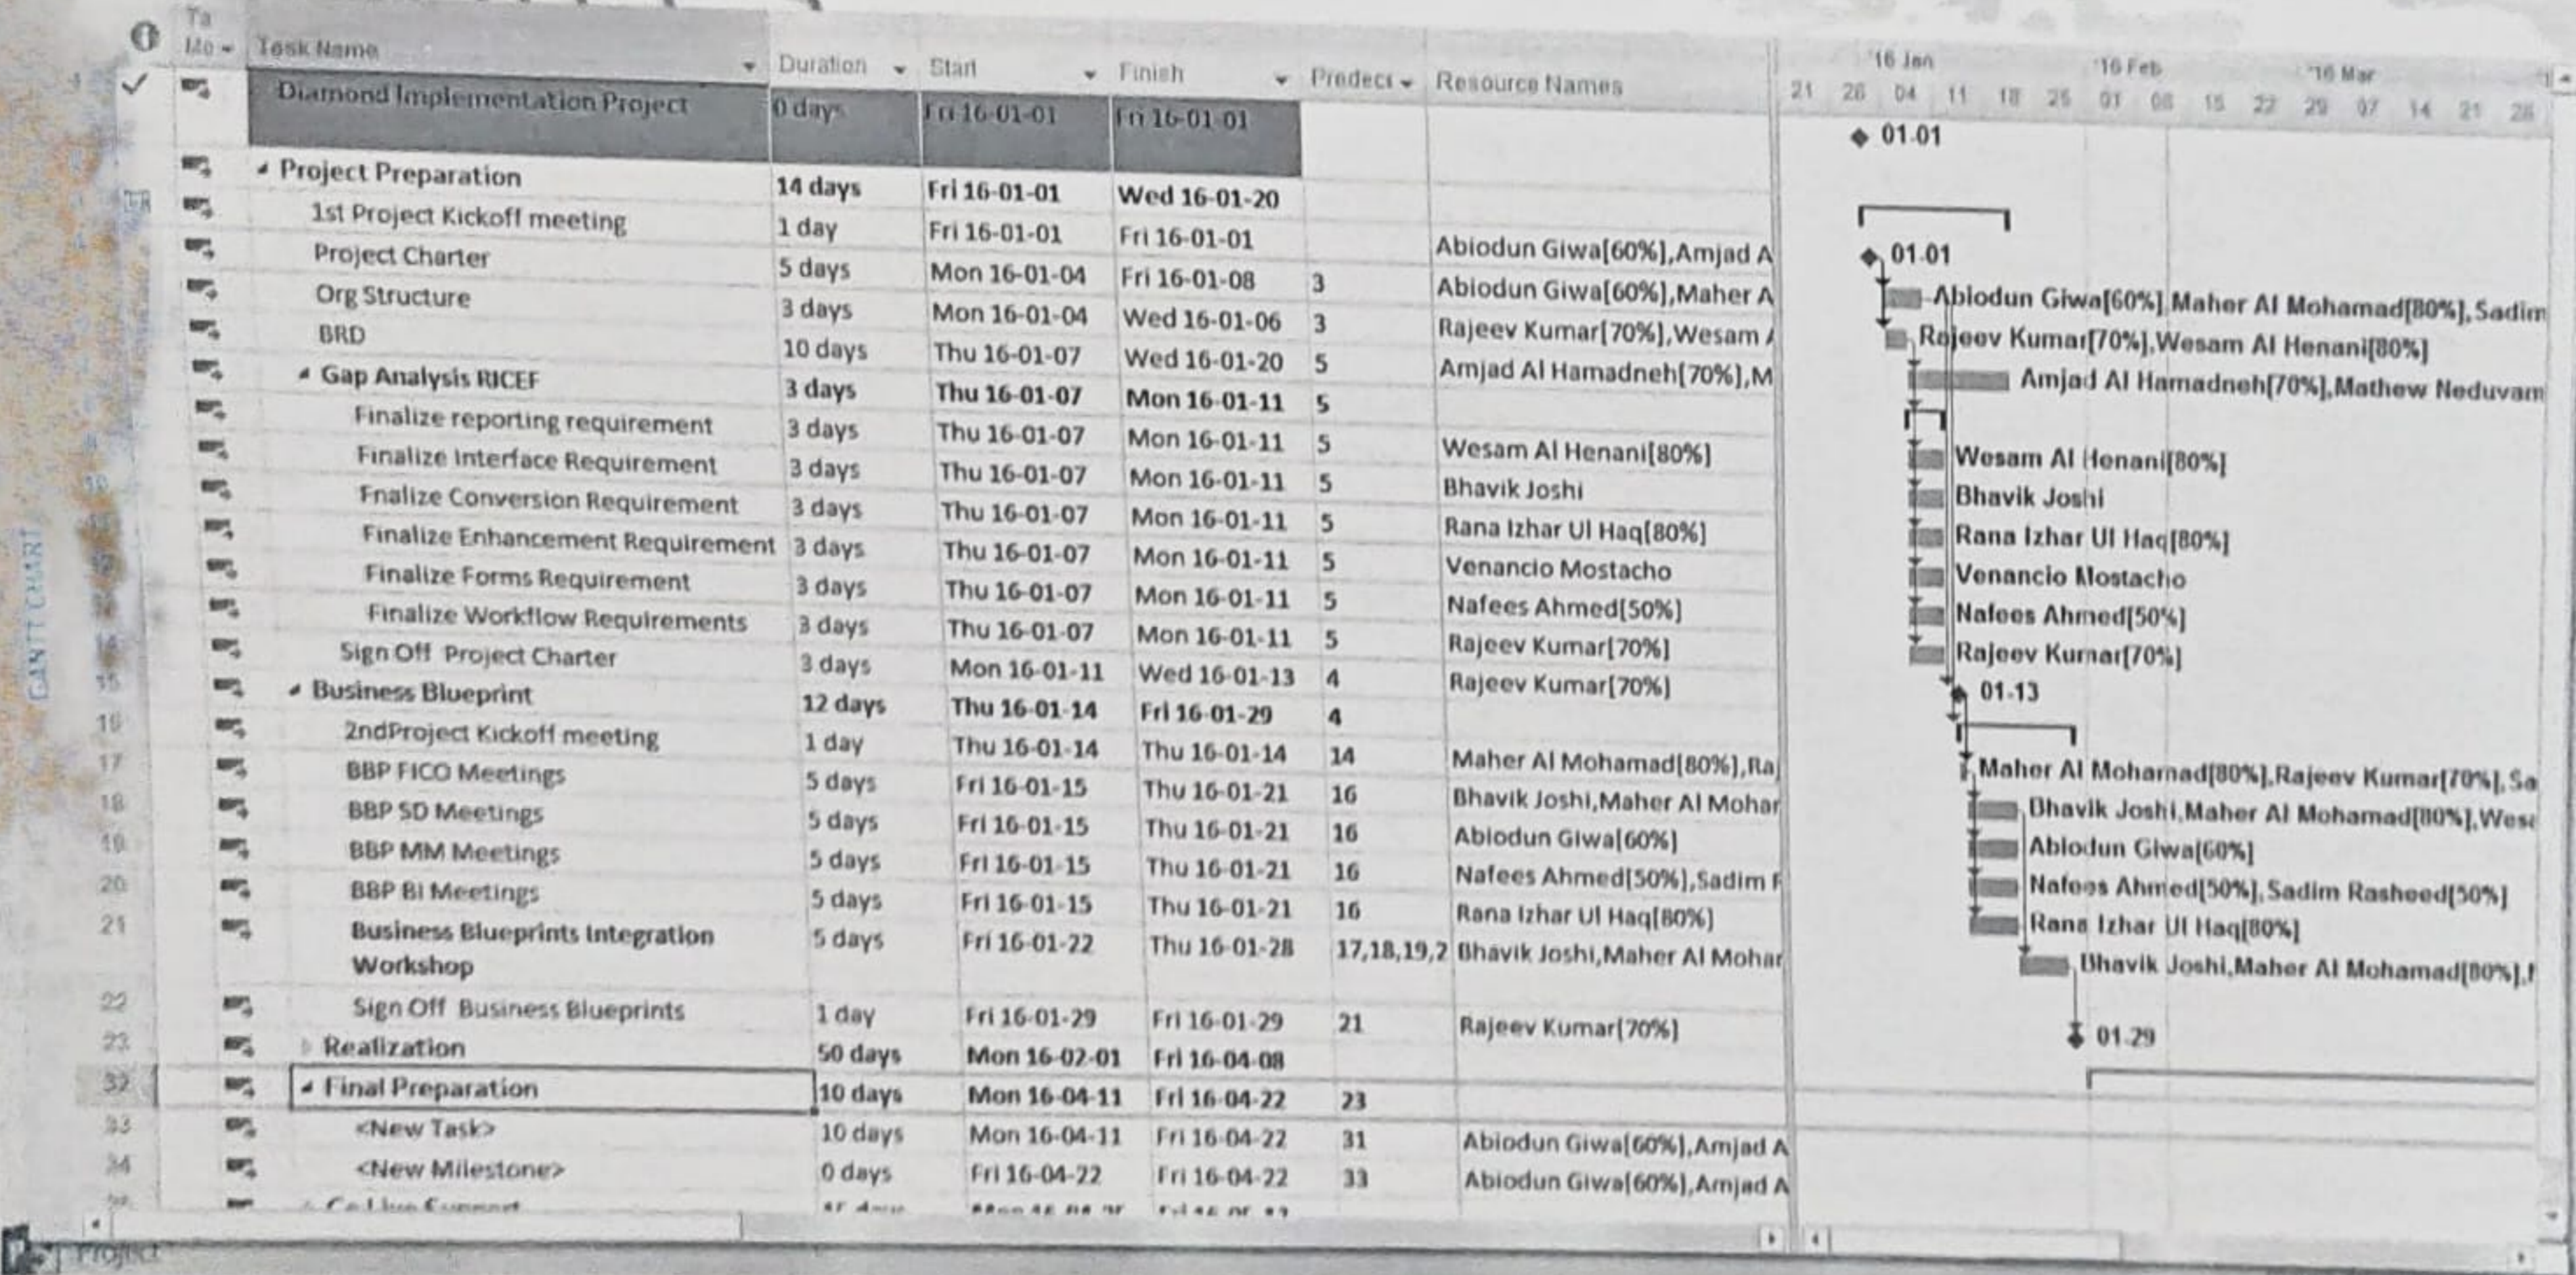

Over allocated Task Resource

| Task ID | Task Name | Duration | Start | Finish | Predecessor | Resource Names | Remaining Work |
|---------|---|----------|--------------|--------------|-------------|--|----------------|
| 1 | Diamond Implementation Project | 0 days | Fri 16-01-01 | Fri 16-01-01 | | | 0 hrs |
| 2 | Project Preparation | 19 days | Fri 16-01-01 | Wed 16-01-27 | | | 136.8 hrs |
| 3 | 1st Project Kickoff meeting | 1 day | Fri 16-01-01 | Fri 16-01-01 | | Abiodun Giwa[60%], Amjad Al Hamadneh[70%], Mathew Neduvamkunnil[70%], Raje | 29.6 hrs |
| 4 | Project Charter | 5 days | Mon 16-01-04 | Fri 16-01-08 | 3 | Abiodun Giwa[60%], Maher Al Mohamad[80%], Sadim Rasheed[50%] | 76 hrs |
| 5 | Org Structure | 3 days | Mon 16-01-04 | Wed 16-01-06 | 3 | Rajeev Kumar[70%], Abiodun Giwa[60%] | 31.2 hrs |
| 6 | This task has overallocated resources. Right-click for options. | 15 days | Thu 16-01-07 | Wed 16-01-27 | 5 | | 0 hrs |
| 7 | | 3 days | Thu 16-01-07 | Mon 16-01-11 | 5 | | 0 hrs |
| 14 | Sign Off Project Charter | 3 days | Mon 16-01-11 | Wed 16-01-13 | 4 | | 0 hrs |

| Task ID | Task Name | Duration | Start | Finish | Predecessor | Resource Names | Remaining Work |
|---------|--------------------------------|----------|--------------|--------------|-------------|--|----------------|
| 1 | Diamond Implementation Project | 0 days | Fri 16-01-01 | Fri 16-01-01 | | | 0 hrs |
| 2 | Project Preparation | 19 days | Fri 16-01-01 | Wed 16-01-27 | | | 141.6 hrs |
| 3 | 1st Project Kickoff meeting | 1 day | Fri 16-01-01 | Fri 16-01-01 | | Abiodun Giwa[60%], Amjad Al Hamadneh[70%], Mathew Neduvamkunnil[70%], Raje | 29.6 hrs |
| 4 | Project Charter | 5 days | Mon 16-01-04 | Fri 16-01-08 | 3 | Abiodun Giwa[60%], Maher Al Mohamad[80%], Sadim Rasheed[50%] | 76 hrs |
| 5 | Org Structure | 3 days | Mon 16-01-04 | Wed 16-01-06 | 3 | Rajeev Kumar[70%], Wesam Al Henani[80%] | 36 hrs |
| 6 | BRD | 15 days | Thu 16-01-07 | Wed 16-01-27 | 5 | | 0 hrs |

Assigning Resources to Tasks

3. Assign Resources Using Resource Tab

The screenshot displays the Microsoft Project interface with the Resource tab selected. The main window shows a Gantt chart and a task list. The 'Assign Resources' dialog box is open, showing the task 'Org Structure' and a list of resources from the 'Project_Basic' project. The resource 'Rajeev Kumar' is selected with 70% units and a cost of \$1,680.00.

Task List:

| Task ID | Task Name | Duration | Start | Finish | Predecessors | Resource Names | Remaining Work |
|---------|-----------------------------------|----------|--------------|--------------|--------------|-----------------------------|----------------|
| 1 | Diamond Implementation Project | 0 days | Fri 16-01-01 | Fri 16-01-01 | | | 0 hrs |
| 2 | Project Preparation | 19 days | Fri 16-01-01 | Wed 16-01-27 | | | 100.6 hrs |
| 3 | 1st Project Kickoff meeting | 1 day | Fri 16-01-01 | Fri 16-01-01 | | Abiodun Giwa[60%], Amjad Al | |
| 4 | Project Charter | 5 days | Mon 16-01-04 | Fri 16-01-08 | 3 | Abiodun Giwa[60%], Maher Al | |
| 5 | Org Structure | 3 days | Mon 16-01-04 | Wed 16-01-06 | 3 | | |
| 6 | BRD | 15 days | Thu 16-01-07 | Wed 16-01-27 | 5 | | |
| 7 | Gap Analysis RICEF | 3 days | Thu 16-01-07 | Mon 16-01-11 | 5 | | |
| 14 | Sign Off Project Charter | 3 days | Mon 16-01-11 | Wed 16-01-13 | 4 | | |
| 15 | Business Blueprint | 12 days | Thu 16-01-14 | Fri 16-01-29 | 4 | | |
| 18 | 2nd Project Kickoff meeting | 1 day | Thu 16-01-14 | Thu 16-01-14 | 14 | | |
| 17 | BBP FICO Meetings | 5 days | Fri 16-01-15 | Thu 16-01-21 | 16 | | |
| 18 | BBP SD Meetings | 5 days | Fri 16-01-15 | Thu 16-01-21 | 16 | | |
| 19 | BBP MM Meetings | 5 days | Fri 16-01-15 | Thu 16-01-21 | 16 | | |
| 20 | BBP BI Meetings | 5 days | Fri 16-01-15 | Thu 16-01-21 | 16 | | |
| 21 | Business Blueprints Integration W | 5 days | Fri 16-01-22 | Thu 16-01-28 | 17,18,19,20 | | |
| 22 | Sign Off Business Blueprints | 1 day | Fri 16-01-29 | Fri 16-01-29 | 21 | | |
| 23 | Realization | 40 days | Mon 16-02-01 | Fri 16-03-25 | | | |
| 24 | Project Team Status Meetings | 10 days | Mon 16-02-01 | Fri 16-02-12 | 22 | | |
| 25 | System Configuration | 30 days | Mon 16-02-15 | Fri 16-03-25 | 24 | | |
| 26 | Training for UT scenarios | 20 days | Mon 16-02-15 | Fri 16-03-11 | 24 | | |
| 27 | RICEF Programs Development | 10 days | Mon 16-02-15 | Fri 16-02-26 | | | |
| 28 | Create RICEF Detailed Definitic | 10 days | Mon 16-02-15 | Fri 16-02-26 | 24,7 | | |

Assign Resources Dialog Box:

Task: Org Structure
 Resource list options: [x]
 Resources from Project_Basic:

| Resource Name | R/D | Units | Cost |
|-------------------|-----|-------|------------|
| ✓ Rajeev Kumar | | 70% | \$1,680.00 |
| Abiodun Giwa | | | |
| Amjad Al Hamadneh | | | |
| Bhavik Joshi | | | |
| Maher Al Mohamad | | | |
| Mathew Neduvamkun | | | |
| Nafees Ahmed | | | |
| Rana Izhar Ul Haq | | | |
| Sadim Rasheed | | | |
| Small client | | | |

Buttons: Assign, Remove, Replace, Graph, Close, Help

Hold down Ctrl and click to select multiple resources

Assigning Resources to Tasks

2. Assign Resources Using Task Information, Resources Tab

| Task No | Task Name | Duration | Start | Finish | Predecessors | Resource Names | Remaining Work |
|---------|-----------------------------------|----------|--------------|--------------|--------------|--|----------------|
| 1 | Diamond Implementation Project | 0 days | Fri 16-01-01 | Fri 16-01-01 | | | |
| 2 | Project Preparation | 19 days | Fri 16-01-01 | Wed 16-01-27 | | | 0 hrs |
| 3 | 1st Project Kickoff meeting | 1 day | Fri 16-01-01 | Fri 16-01-01 | | | 29.6 hrs |
| 4 | Project Charter | 5 days | Mon 16-01-04 | Fri 16-01-08 | 3 | Abiodun Giwa[60%], Amjad Al Hamadneh[70%], Mathew Neduvamkunnil[70%], Raje | 29.6 hrs |
| 5 | Org Structure | 3 days | Mon 16-01-04 | Wed 16-01-06 | | | 0 hrs |
| 6 | BRD | 15 days | Thu 16-01-07 | Wed 16-01-21 | | | |
| 7 | Gap Analysis RICEF | 3 days | Thu 16-01-07 | Mon 16-01-11 | | | |
| 14 | Sign Off Project Charter | 3 days | Mon 16-01-11 | Wed 16-01-15 | | | |
| 15 | Business Blueprint | 12 days | Thu 16-01-14 | Fri 16-01-29 | | | |
| 16 | 2nd Project Kickoff meeting | 1 day | Thu 16-01-14 | Thu 16-01-14 | | | |
| 17 | BBP FICO Meetings | 5 days | Fri 16-01-15 | Thu 16-01-22 | | | |
| 18 | BBP SD Meetings | 5 days | Fri 16-01-15 | Thu 16-01-22 | | | |
| 19 | BBP MM Meetings | 5 days | Fri 16-01-15 | Thu 16-01-22 | | | |
| 20 | BBP BI Meetings | 5 days | Fri 16-01-15 | Thu 16-01-22 | | | |
| 21 | Business Blueprints Integration W | 5 days | Fri 16-01-22 | Thu 16-01-29 | | | |
| 22 | Sign Off Business Blueprints | 1 day | Fri 16-01-29 | Fri 16-01-29 | | | |
| 23 | Realization | 40 days | Mon 16-02-01 | Fri 16-03-25 | | | |
| 24 | Project Team Status Meetings | 10 days | Mon 16-02-01 | Fri 16-02-12 | | | |
| 25 | System Configuration | 30 days | Mon 16-02-15 | Fri 16-03-25 | | | |
| 26 | Training for UT scenarios | 20 days | Mon 16-02-15 | Fri 16-03-11 | | | |
| 27 | RICEF Programs Development | 10 days | Mon 16-02-15 | Fri 16-02-26 | | | |
| 28 | Create RICEF Detailed Definitic | 10 days | Mon 16-02-15 | Fri 16-02-26 | | | |
| 29 | Create RICEF Programs | 10 days | Mon 16-02-15 | Fri 16-02-26 | | | |
| 30 | Test and Review RICEF Program | 10 days | Mon 16-02-15 | Fri 16-02-26 | | | |

Task Information

General | Predecessors | Resources | Advanced | Notes | Custom Fields

Name: Duration: Estimated

Resources:

| Resource Name | Assignment Owner | Units | Cost |
|----------------------|------------------|-------|------|
| Abiodun Giwa | | 60% | |
| Maher Al Mohamad | | 80% | |
| Sadim Rasheed | | 50% | |
| Abiodun Giwa | | | |
| Amjad Al Hamadneh | | | |
| Bhavik Joshi | | | |
| Maher Al Mohamad | | | |
| Mathew Neduvamkunnil | | | |
| Nafees Ahmed | | | |
| Rajeev Kumar | | | |
| Rana Izhar Ul Haq | | | |
| Sadim Rasheed | | | |
| Sunil Singh | | | |
| Venancio Mostacho | | | |
| Wesam Al Henani | | | |

OK Cancel

Calendar View

2015 December

| M | T | W | T | F | S | S |
|----|----|----|----|----|----|----|
| | 1 | 2 | 3 | 4 | 5 | 6 |
| 7 | 8 | 9 | 10 | 11 | 12 | 13 |
| 14 | 15 | 16 | 17 | 18 | 19 | 20 |
| 21 | 22 | 23 | 24 | 25 | 26 | 27 |
| 28 | 29 | 30 | 31 | | | |

2016 January

| M | T | W | T | F | S | S |
|----|----|----|----|----|----|----|
| | | | 1 | 2 | 3 | |
| 4 | 5 | 6 | 7 | 8 | 9 | 10 |
| 11 | 12 | 13 | 14 | 15 | 16 | 17 |
| 18 | 19 | 20 | 21 | 22 | 23 | 24 |
| 25 | 26 | 27 | 28 | 29 | 30 | 31 |

2016 February

| M | T | W | T | F | S | S |
|----|----|----|----|----|----|----|
| 1 | 2 | 3 | 4 | 5 | 6 | 7 |
| 8 | 9 | 10 | 11 | 12 | 13 | 14 |
| 15 | 16 | 17 | 18 | 19 | 20 | 21 |
| 22 | 23 | 24 | 25 | 26 | 27 | 28 |
| 29 | | | | | | |

Month Week Custom

2016 January

| Monday | Tuesday | Wednesday | Thursday | Friday | Saturday | Sunday |
|----------------------------|---------|-----------|--|--|---------------------------|--------|
| 28 | 29 | 30 | 31 | Jan 01 | 02 | 03 |
| | | | | Diamond Implementation 1st Project Kickoff meet | | |
| 04 | 05 | 06 | 07 | 08 | 09 | 10 |
| Org Structure, 3 days | | | BRD, 10 days | | | |
| Project Charter, 5 days | | | Finalize reporting requirement, 3 days | | | |
| | | | Finalize Interface Requirement, 3 days | | | |
| | | | Finalize Conversion Requirement, 3 days | | | |
| 11 | 12 | 13 | 14 | 15 | 16 | 17 |
| Sign Off Project Charter | | | BRD, 10 days | | | |
| Finalize reporting require | | | 2nd Project Kickoff meet | | BBP FICO Meetings, 5 days | |
| Finalize Interface Require | | | | | BBP SD Meetings, 5 days | |
| Finalize Conversion Requ | | | | | BBP MM Meetings, 5 days | |
| 18 | 19 | 20 | 21 | 22 | 23 | 24 |
| BRD, 10 days | | | BBP BI Meetings, 5 days | | | |
| BBP FICO Meetings, 5 days | | | Business Blueprints Integration Workshop, 5 days | | | |
| BBP SD Meetings, 5 days | | | | | | |
| BBP MM Meetings, 5 days | | | | | | |

CALENDAR

Team Planner View

Resource Name

Un 16 January
Ta

2016 February

2016 March

2016 April

Rajeev Kumar

Maheer Al Mohamad

Mathew Neduvamkunnil

Sadim Rasheed

Amjad Al Hamadneh

Rana Izhar Ul Haq

Wesam Al Henani

Venancio Mostacho

Abiodun Giwa

Bhavik Joshi

Sunil Singh

Nafees Ahmed

TEAM PLANNER

Org Str Finaliz Workfl Sig Off Project Team Status Meetings

Project Charter BBP FICO Meetings Business Blueprints Project Team Status Meetings

BRD Project Charter BBP MM Meetings Business Blueprints Project Team Status Meetings

BRD Finalize Conver BBP BI Meetings Business Blueprints Project Team Status Meetings

Org Str Finaliz reportl Finaliz Enhanc BBP FICO Meetings Business Blueprints Project Team Status Meetings

Project Charter BBP SD Meetings Business Blueprints Project Team Status Meetings

Finaliz Interfac BBP FICO Meetings Business Blueprints Project Team Status Meetings

BRD Finaliz Forms BBP MM Meetings Business Blueprints Project Team Status Meetings

Training for UT scenarios

System Configuration

System Configuration

Training for UT scenarios

System Configuration

Training for UT scenarios

Create RICEF Detailed

Test and Review RICEF Programs

Test and Review RICEF Programs

Test and Review RICEF Programs

Test and Review RICEF Programs

Integration Test

Integration Test

Integration Test

Integration Test

Integration Test

<New Task>

<New Task>

<New Task>

<New Task>

<New Task>

<New Task>

<New Task>

<New Task>

<New Task>

<New Task>

<New Task>

<New Task>

<New Task>

<New Task>

<New Task>

<New Task>

<New Task>

<New Task>

<New Task>

<New Task>

<New Task>

<New Task>

<New Task>

<New Task>

Unassigned Tasks 0

Resources Using View

| Resource Name | | Work | Details | Sun Jan 31 | Mon Feb 01 | Tue Feb 02 | Wed Feb 03 | Thu Feb 04 | Fri Feb 05 | Sat Feb 06 | Sun Feb 07 | Mon Feb 08 |
|---------------|--------------------------------|-------------|---------|------------|------------|------------|------------|------------|------------|------------|------------|------------|
| | | | | 12 PM | 12 AM | 12 PM | 12 AM | 12 PM | 12 AM | 12 PM | 12 AM | 12 PM |
| | Group: No Value | 0 hrs | Work | | | | | | | | | |
| | ↳ Unassigned | 0 hrs | Work | | | | | | | | | |
| | Group: ABAP | 432 hrs | Work | | | | | | | | | |
| 8 | ↳ Venancio Mostacho | 432 hrs | Work | | 4h | 4h | 4h | 4h | 4h | 4h | 4h | 4h |
| | Group: BI | 307.2 hrs | Work | | 4h | 4h | 4h | 4h | 4h | 4h | 4h | 4h |
| 6 | ↳ Rana Izhar Ul Haq | 307.2 hrs | Work | | 3.2h | 3.2h | 3.2h | 3.2h | 3.2h | 3.2h | 3.2h | 3.2h |
| | Group: FICO | 1,830.4 hrs | Work | | 3.2h | 3.2h | 3.2h | 3.2h | 3.2h | 3.2h | 3.2h | 3.2h |
| 2 | ↳ Maher Al Mohamad | 454.4 hrs | Work | | 13.2h | 13.2h | 13.2h | 13.2h | 13.2h | 13.2h | 13.2h | 13.2h |
| 5 | ↳ Amjad Al Hamadneh | 425.6 hrs | Work | | 3.2h | 3.2h | 3.2h | 3.2h | 3.2h | 3.2h | 3.2h | 3.2h |
| 7 | ↳ Wesam Al Henani | 486.4 hrs | Work | | 2.8h | 2.8h | 2.8h | 2.8h | 2.8h | 2.8h | 2.8h | 2.8h |
| 10 | ↳ Bhavik Joshi | 464 hrs | Work | | 3.2h | 3.2h | 3.2h | 3.2h | 3.2h | 3.2h | 3.2h | 3.2h |
| | Group: MM | 1,244 hrs | Work | | 4h | 4h | 4h | 4h | 4h | 4h | 4h | 4h |
| 4 | ↳ Sadim Rasheed | 324 hrs | Work | | 8h | 8h | 8h | 8h | 8h | 8h | 8h | 8h |
| 11 | ↳ Sunil Singh | 608 hrs | Work | | 2h | 2h | 2h | 2h | 2h | 2h | 2h | 2h |
| 12 | ↳ Nafees Ahmed | 312 hrs | Work | | 4h | 4h | 4h | 4h | 4h | 4h | 4h | 4h |
| | Group: PM | 263.2 hrs | Work | | 2h | 2h | 2h | 2h | 2h | 2h | 2h | 2h |
| 1 | ↳ Rajeev Kumar | 263.2 hrs | Work | | 2.8h | 2.8h | 2.8h | 2.8h | 2.8h | 2.8h | 2.8h | 2.8h |
| | Group: SD | 838.4 hrs | Work | | 2.8h | 2.8h | 2.8h | 2.8h | 2.8h | 2.8h | 2.8h | 2.8h |
| 3 | ↳ Mathew Neduvamkunnil | 425.6 hrs | Work | | 5.2h | 5.2h | 5.2h | 5.2h | 5.2h | 5.2h | 5.2h | 5.2h |
| 9 | ↳ Abiodun Giwa | 412.8 hrs | Work | | 2.8h | 2.8h | 2.8h | 2.8h | 2.8h | 2.8h | 2.8h | 2.8h |
| | ↳ 1st Project Kickoff meeting | 4.8 hrs | Work | | 2.4h | 2.4h | 2.4h | 2.4h | 2.4h | 2.4h | 2.4h | 2.4h |
| | ↳ Project Charter | 24 hrs | Work | | | | | | | | | 2.4h |
| | ↳ BBP SD Meetings | 24 hrs | Work | | | | | | | | | |
| | ↳ Project Team Status Meetings | 48 hrs | Work | | | | | | | | | |
| | ↳ System Configuration | 144 hrs | Work | | 2.4h | 2.4h | 2.4h | 2.4h | 2.4h | 2.4h | 2.4h | 2.4h |
| | ↳ Integration Test | 48 hrs | Work | | | | | | | | | 2.4h |
| | ↳ <New Task> | 48 hrs | Work | | | | | | | | | |
| | ↳ <New Milestone> | 0 hrs | Work | | | | | | | | | |

RESOURCE USAGE

Resources Form

Name: Rajesh Kumar Initials: R Max units: 1000 Previous Next

Costs

Std rate: \$100.00/h Per use: \$0.00 Base cat: Standard

Ovt rate: \$175.00/h Accru at: Prorated Group: PM Code:

| Project | ID | Task Name | Work | Leveling Delay | Delay | Scheduled Start | Scheduled Finish |
|---------------|----|--------------------------------|-------|----------------|-------|-----------------|------------------|
| Project_Basic | 14 | Sign Off Project Charter | 16.8h | 0d | 0d | Mon 16-01-11 | Wed 16-01-13 |
| Project_Basic | 22 | Sign Off Business Blueprints | 5.6h | 0d | 0d | Fri 16-01-29 | Fri 16-01-29 |
| Project_Basic | 3 | 1st Project Kickoff meeting | 5.6h | 0d | 0d | Fri 16-01-01 | Fri 16-01-01 |
| Project_Basic | 5 | Org Structure | 16.8h | 0d | 0d | Mon 16-01-04 | Wed 16-01-06 |
| Project_Basic | 13 | Finalize Workflow Requirements | 16.8h | 0d | 0d | Thu 16-01-07 | Mon 16-01-11 |
| Project_Basic | 16 | 2ndProject Kickoff meeting | 5.6h | 0d | 0d | Thu 16-01-14 | Thu 16-01-14 |
| Project_Basic | 24 | Project Team Status Meetings | 56h | 0d | 0d | Mon 16-02-01 | Fri 16-02-12 |
| Project_Basic | 33 | <New Task> | 56h | 0d | 0d | Mon 16-04-11 | Fri 16-04-22 |
| Project_Basic | 34 | <New Milestone> | 0h | 0d | 0d | Fri 16-04-22 | Fri 16-04-22 |
| Project_Basic | 36 | <New Task> | 56h | 0d | 0d | Mon 16-04-25 | Fri 16-05-06 |
| Project_Basic | 37 | Project Closure | 28h | 0d | 0d | Mon 16-05-09 | Fri 16-05-13 |

Task Form


Name: 1st Project Kickoff meeting Duration: 1 day Effort driven Manually Scheduled Previous Next

Start: Fri 16-01-01 Finish: Fri 16-01-01 Task type: Fixed Units % Complete: 0%

| ID | Resource Name | Work | R/D | Leveling Delay | Delay | Scheduled Start | Scheduled Finish |
|----|----------------------|------|-----|----------------|-------|-----------------|------------------|
| 9 | Abiodun Gwa | 4.8h | | 0d | 0d | Fri 16-01-01 | Fri 16-01-01 |
| 5 | Amjad Al Hamadneh | 5.6h | | 0d | 0d | Fri 16-01-01 | Fri 16-01-01 |
| 3 | Mathew Neduvamkunnil | 5.6h | | 0d | 0d | Fri 16-01-01 | Fri 16-01-01 |
| 1 | Rajeev Kumar | 5.6h | | 0d | 0d | Fri 16-01-01 | Fri 16-01-01 |
| 11 | Sunil singh | 8h | | 0d | 0d | Fri 16-01-01 | Fri 16-01-01 |

TASK FORM

Network Diagram View

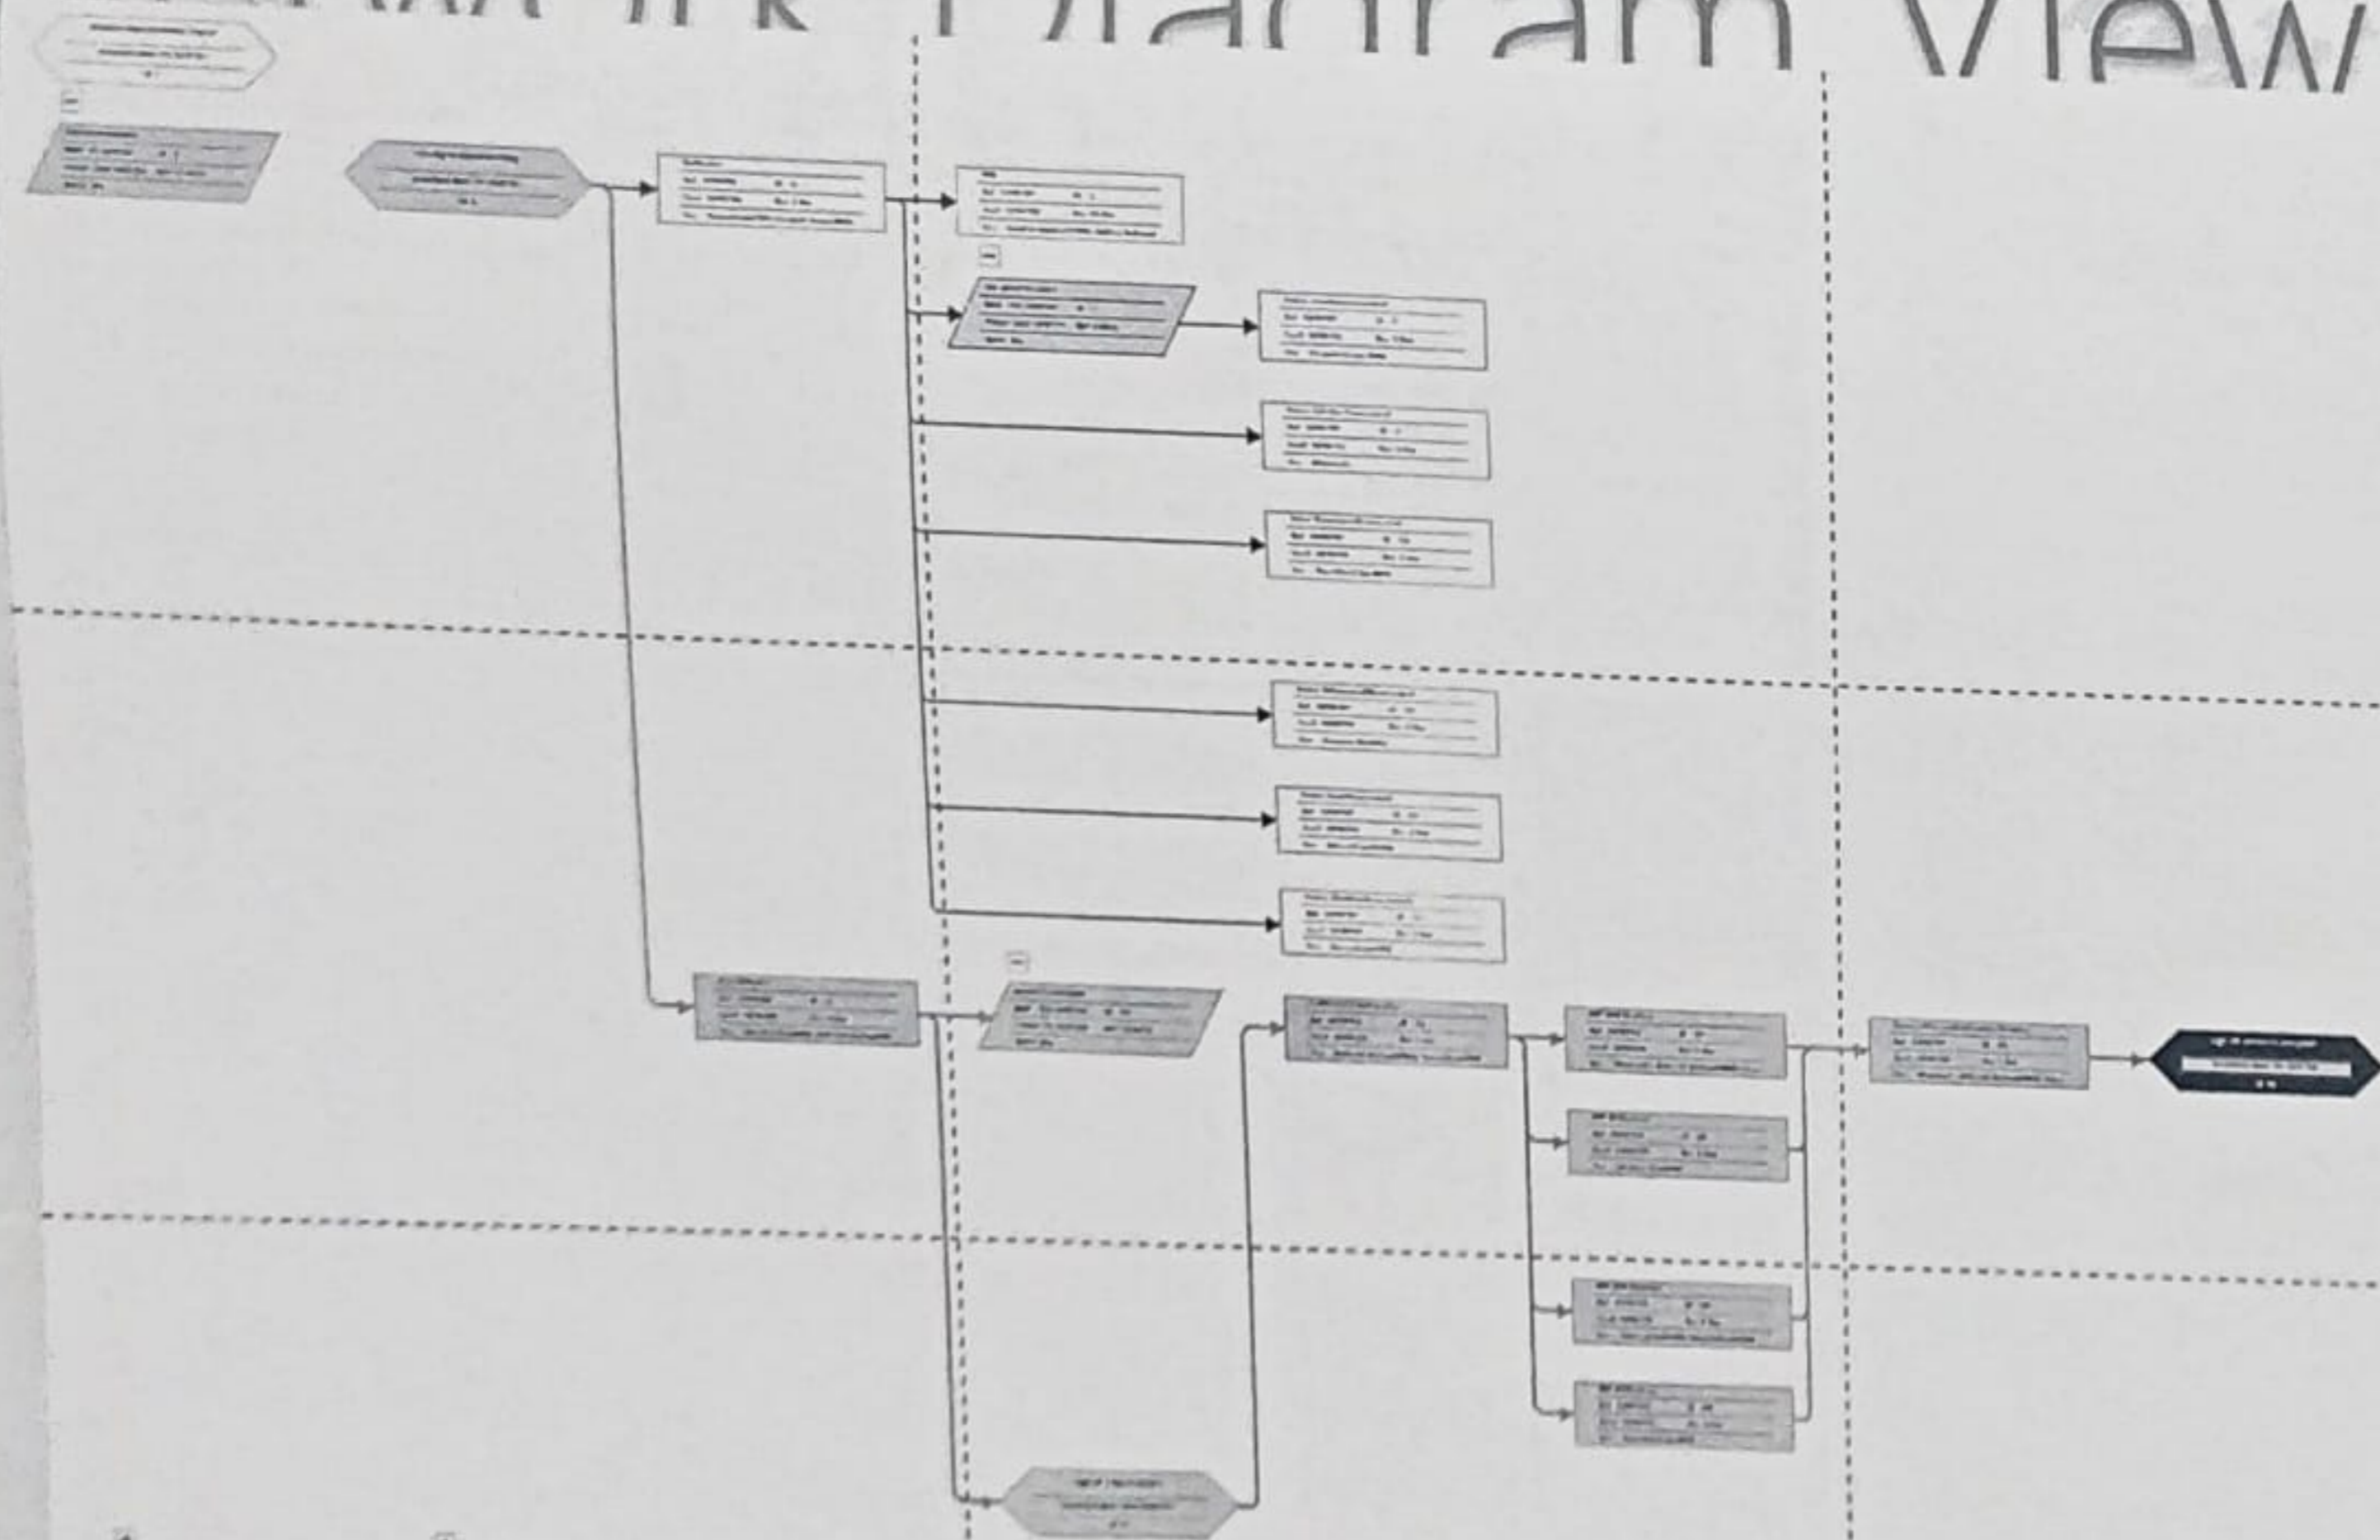


Cost Overruns Report

COST OVERRUNS


TASK COST VARIANCE

Cost variance for all top-level tasks in the project.

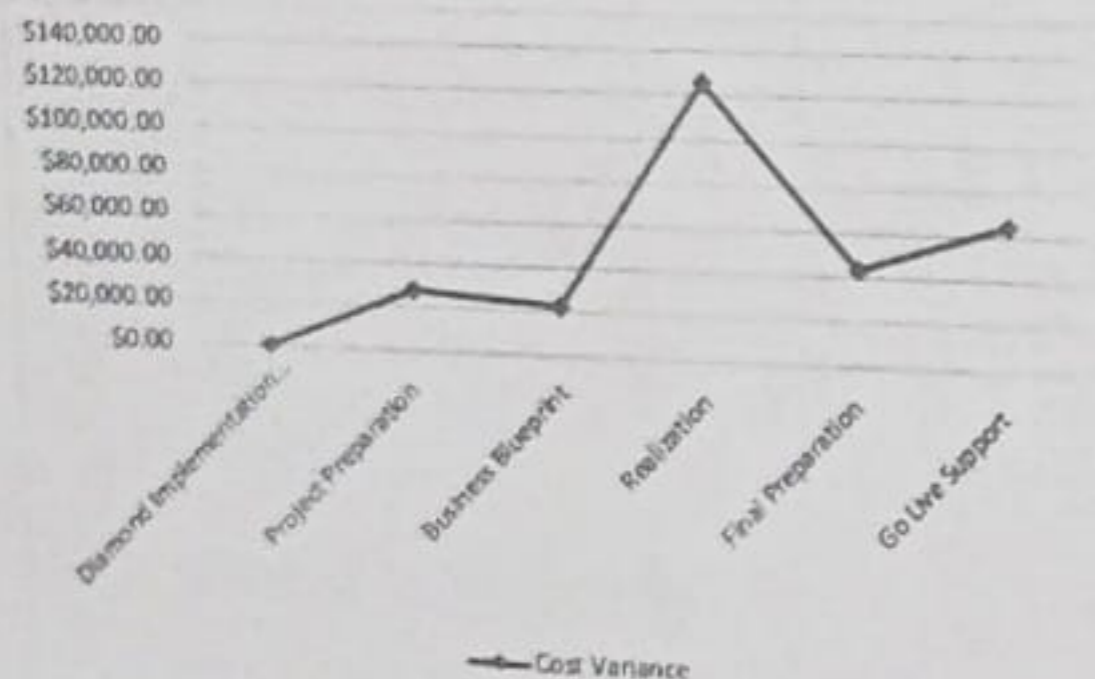

RESOURCE COST VARIANCE

Cost variance for all the work resources.

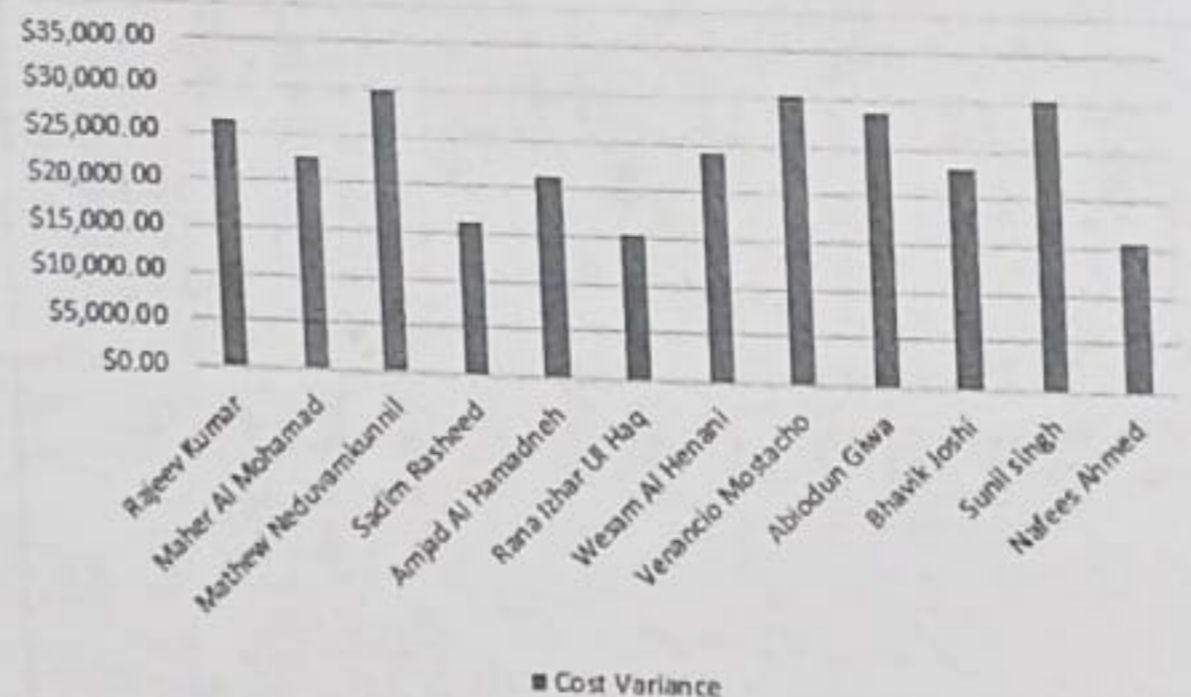

| Name | % Complete | Cost | Baseline Cost | Cost Variance |
|--------------------------------|------------|-------------|---------------|---------------|
| Diamond Implementation Project | 100% | \$0.00 | \$0.00 | \$0.00 |
| Project Preparation | 0% | \$28,368.00 | \$0.00 | \$28,368.00 |
| Business Blueprint | 0% | \$22,680.00 | \$0.00 | \$22,680.00 |


| Name | Cost | Baseline Cost | Cost Variance |
|----------------------|-------------|---------------|---------------|
| Rajeev Kumar | \$26,320.00 | \$0.00 | \$26,320.00 |
| Maher Al Mohamad | \$22,720.00 | \$0.00 | \$22,720.00 |
| Mathew Neduvamkunnil | \$29,792.00 | \$0.00 | \$29,792.00 |
| Sadim Rasheed | \$16,200.00 | \$0.00 | \$16,200.00 |
| Amjad Al Hamadneh | \$21,280.00 | \$0.00 | \$21,280.00 |

Resource Overview Report

RESOURCE OVERVIEW

RESOURCE STATS

Work status for all work resources.

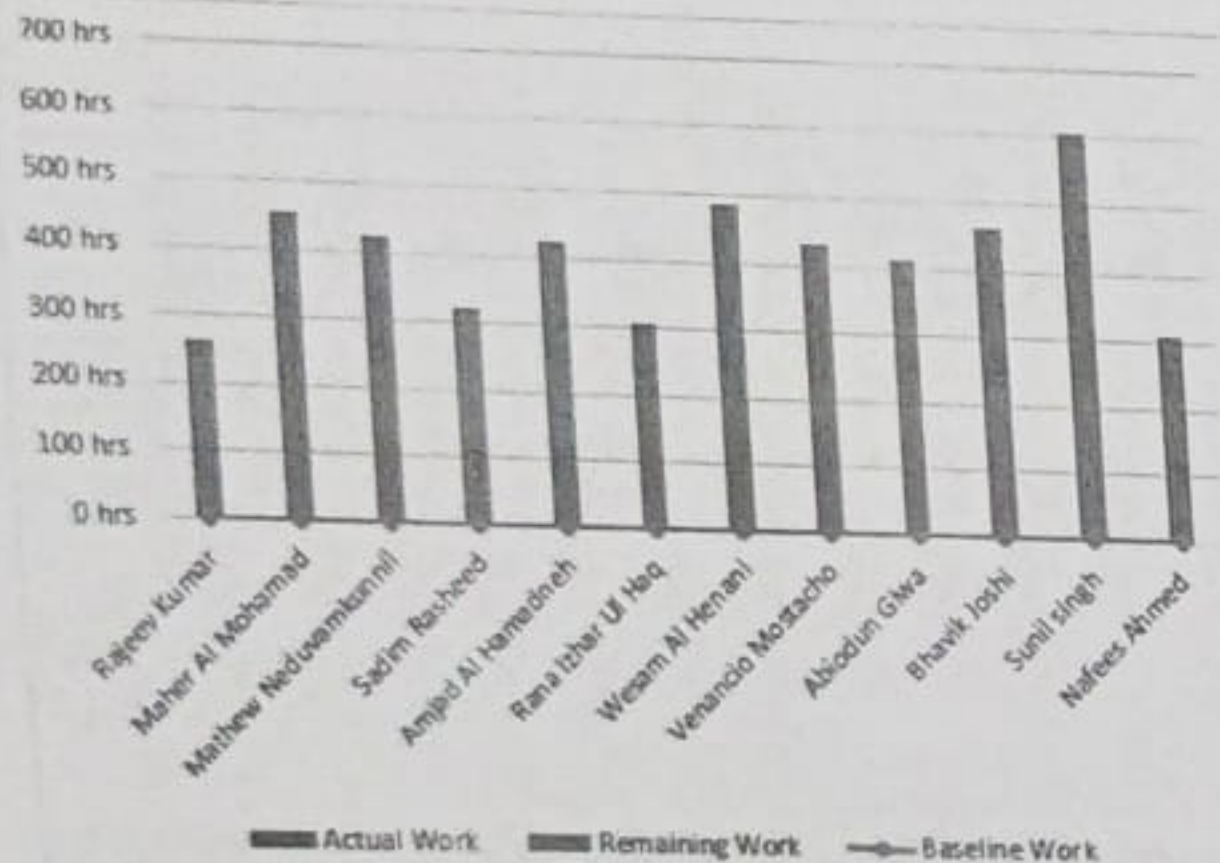

RESOURCE STATUS

Remaining work for all work resources.

| Name | Start | Finish | Remaining Work |
|----------------------|--------------|--------------|----------------|
| Rajeev Kumar | Fri 16-01-01 | Fri 16-05-13 | 263.2 hrs |
| Maher Al Mohamad | Mon 16-01-04 | Fri 16-05-13 | 454.4 hrs |
| Mathew Neduvamkunnil | Fri 16-01-01 | Fri 16-05-13 | 425.6 hrs |
| Sadim Rasheed | Mon 16-01-04 | Fri 16-05-13 | 324 hrs |
| Amjad Al Hamadneh | Fri 16-01-01 | Fri 16-05-13 | 425.6 hrs |
| Rana Izhar Ul Haq | Thu 16-01-07 | Fri 16-05-13 | 307.2 hrs |
| Wesam Al Henani | Mon 16-01-04 | Fri 16-05-13 | 486.4 hrs |
| Venancio Mostacho | Thu 16-01-07 | Fri 16-05-13 | 432 hrs |
| Abiodun Giwa | Fri 16-01-01 | Fri 16-05-13 | 412.8 hrs |
| Bhavik Joshi | Thu 16-01-07 | Fri 16-05-13 | 464 hrs |
| Sunil singh | Fri 16-01-01 | Fri 16-05-13 | 608 hrs |
| Nafees Ahmed | Thu 16-01-07 | Fri 16-05-13 | 312 hrs |

Printing the Project Map

Print

Printer: HP DesignJet F4222 WF

Settings

Print: Enter Project

Pages: 1 to 1

Landscape Orientation

Print

Page Setup

Page | Margins | Headers | Footers | Layout | View

Orientation: Portrait Landscape

Scaling: Adjust to fit Page number All

Other: Paper size: A4, Page number: Auto

Print

